MASTER DELIVERABLES LIST

81 DELIVERABLES · 5 LEVELS, 6 SLABS · STATUS DERIVED AT BUILD TIME

CODE	CL	STATUS	DELIVERABLE	SCALE
PACKAGE 0 — INFORMATION REQUIRED FROM OTHERS (3)				
SUR-001	X	· not started	Measured topographic and boundary survey	1:200
GEO-001	X	! blocked	Soil investigation and foundation recommendation	-
CLI-001	D	+ issued	Client instructions and decisions record	-
PACKAGE A — PRESENTATION AND ESTIMATION (8)				
A-01	D	+ issued	Exterior views - axonometric, three schemes	1:250
A-02	D	· not started	Interior cutaway axonometric - ground floor, +0.00	1:100
A-03	D	· not started	Interior cutaway axonometric - first floor, +3.30	1:100
A-04	D	· not started	Interior cutaway axonometric - second floor, +6.60	1:100
A-05	D	· not started	Interior cutaway axonometric - third floor, +9.90	1:100
A-06	D	· not started	Interior cutaway axonometric - penthouse floor, +13.20	1:100
A-07	D	· not started	Architectural design brief	-
A-08	X	! blocked	Cost estimation report - elemental	-
PACKAGE B — ARCHITECTURE (21)				
ARC-000	D	+ issued	Master deliverables list and document register	-
ARC-001	D	· not started	Cover sheet, project data and drawing index	-
ARC-002	L	· not started	General notes, symbols and code compliance matrix	-
ARC-100	D	+ issued	Context and master site plan	1:75
ARC-101	D	+ issued	Ground floor plan, +0.00	1:50
ARC-102	D	+ issued	First floor plan, +3.30	1:50
ARC-103	D	+ issued	Second floor plan, +6.60	1:50
ARC-104	D	+ issued	Third floor plan, +9.90	1:50
ARC-105	D	+ issued	Penthouse floor plan, +13.20	1:50
ARC-106	D	+ issued	Roof plan over the penthouse, +16.45	1:50
ARC-200	D	+ issued	Facade elevations - all four faces, scheme A	1:50 / 1:75
ARC-300	D	+ issued	Longitudinal section A-A	1:50
ARC-301	D	+ issued	Transverse section B-B	1:50
ARC-400	D	+ issued	Reflected ceiling plan - ground floor, +0.00	1:50
ARC-401	D	+ issued	Reflected ceiling plan - first floor, +3.30	1:50
ARC-402	D	+ issued	Reflected ceiling plan - second floor, +6.60	1:50
ARC-403	D	+ issued	Reflected ceiling plan - third floor, +9.90	1:50
ARC-404	D	+ issued	Reflected ceiling plan - penthouse floor, +13.20	1:50
ARC-500	D	+ issued	Door and window schedule	1:100
ARC-600	L	· not started	Construction details	1:5 / 1:10
ARC-700	D	+ issued	External works and landscape	1:75
PACKAGE C — STRUCTURE (12)				
STR-001	L	· not started	Structural notes, materials and design criteria	-
STR-100	L	! blocked	Excavation, grading and shoring	1:100
STR-101	L	! blocked	Foundation layout	1:50
STR-200	L	· not started	Column schedule and grid	1:50
STR-301	L	! blocked	Slab framing layout at +0.00	1:50
STR-302	L	! blocked	Slab framing layout at +3.30	1:50
STR-303	L	! blocked	Slab framing layout at +6.60	1:50
STR-304	L	! blocked	Slab framing layout at +9.90	1:50
STR-305	L	! blocked	Slab framing layout at +13.20	1:50
STR-306	L	! blocked	Slab framing layout at +16.45	1:50
STR-400	L	! blocked	Retaining and boundary walls	1:50
STR-500	L	! blocked	Cantilever balcony structure	1:20
PACKAGE D — BUILDING SERVICES (33)				
EL-100	L	· not started	Power and small power layout - ground floor, +0.00	1:50
EL-101	L	· not started	Power and small power layout - first floor, +3.30	1:50
EL-102	L	· not started	Power and small power layout - second floor, +6.60	1:50
EL-103	L	· not started	Power and small power layout - third floor, +9.90	1:50
EL-104	L	· not started	Power and small power layout - penthouse floor, +13.20	1:50
EL-200	L	· not started	Lighting and switching layout - ground floor, +0.00	1:50
EL-201	L	· not started	Lighting and switching layout - first floor, +3.30	1:50
EL-202	L	· not started	Lighting and switching layout - second floor, +6.60	1:50
EL-203	L	· not started	Lighting and switching layout - third floor, +9.90	1:50
EL-204	L	· not started	Lighting and switching layout - penthouse floor, +13.20	1:50
EL-300	L	· not started	Low voltage, data and security layout - ground floor, +0.00	1:50
EL-301	L	· not started	Low voltage, data and security layout - first floor, +3.30	1:50
EL-302	L	· not started	Low voltage, data and security layout - second floor, +6.60	1:50
EL-303	L	· not started	Low voltage, data and security layout - third floor, +9.90	1:50
EL-304	L	· not started	Low voltage, data and security layout - penthouse floor, +13.20	1:50
ME-100	L	· not started	HVAC layout - ground floor, +0.00	1:50
ME-101	L	· not started	HVAC layout - first floor, +3.30	1:50
ME-102	L	· not started	HVAC layout - second floor, +6.60	1:50
ME-103	L	· not started	HVAC layout - third floor, +9.90	1:50
ME-104	L	· not started	HVAC layout - penthouse floor, +13.20	1:50
PL-100	L	· not started	Water supply layout - ground floor, +0.00	1:50
PL-101	L	· not started	Water supply layout - first floor, +3.30	1:50
PL-102	L	· not started	Water supply layout - second floor, +6.60	1:50
PL-103	L	· not started	Water supply layout - third floor, +9.90	1:50
PL-104	L	· not started	Water supply layout - penthouse floor, +13.20	1:50
PL-200	L	· not started	Drainage layout - ground floor, +0.00	1:50
PL-201	L	· not started	Drainage layout - first floor, +3.30	1:50
PL-202	L	· not started	Drainage layout - second floor, +6.60	1:50
PL-203	L	· not started	Drainage layout - third floor, +9.90	1:50
PL-204	L	· not started	Drainage layout - penthouse floor, +13.20	1:50
EL-400	L	! blocked	Electrical single line diagram	Schematic
ME-200	L	! blocked	HVAC schematic and plant arrangement	Schematic
PL-300	L	! blocked	Drainage and water riser diagram	Schematic
PACKAGE E — QUANTITIES AND COST CONTROL (4)				
QS-001	D	· not started	Bill of quantities - itemised, unpriced, by trade	-
QS-002	D	! blocked	Bill of materials	-
QS-003	L	! blocked	Material requisitions and specifications	-
QS-004	X	! blocked	Owner's cost baseline	-

+ ISSUED > IN PROGRESS ! BLOCKED · NOT STARTED

MASTER DELIVERABLES LIST

DOCUMENT CONTROL · PACKAGES 0 AND A TO E · STATUS DERIVED

THE SET AT A GLANCE

DELIVERABLES	81
ISSUED	20
IN PROGRESS	0
BLOCKED	18
NOT STARTED	43
LEVELS	5
STRUCTURAL SLABS	6
D — DERIVED	29
L — LAYOUT FOR OTHERS	48
X — EXTERNAL	4

GENERAL NOTES

1. Nothing is issued as engineering that has not been engineered. Class D is generated from geometry.py and is ours to issue. Class L is layout and coordination only, sized and certified by others. Class X cannot be produced here at all.

2. So the structural package carries foundation layouts on the real grid and column coordinates, and no reinforcement; the services package carries coordination layouts, and no load calculations.

3. Status is derived at build time from the issued set, never typed. A row naming a sheet nobody draws, or a document nobody writes, fails the checks rather than printing here.

4. Five levels, 6 structural slabs: the slab at +13.20 is the penthouse floor and the roof over the third floor at once.

5. Deliverable codes are the client's. Where one resolves to sheets already issued, the existing number is the cross reference — the agreed set is not renumbered. The prefix is part of the number: A-402 is the street elevation and ARC-402 the second floor's ceiling plan, and they are different sheets.

6. The exterior is settled: scheme A, adopted at P18. Blocked rows now wait on the measured survey and the plot's soil figures, neither of which can be settled from the drawings.

7. For the owner's own record, costing and construction information. Not a tender issue, and not for construction.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


MASTER DELIVERABLES LIST

DRAWING No	REVISION	SCALE	DATE
ARC-000	**P19**	**NTS**	**2026-10-07**

Document control — every status on this sheet is derived at build time from the issued set.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

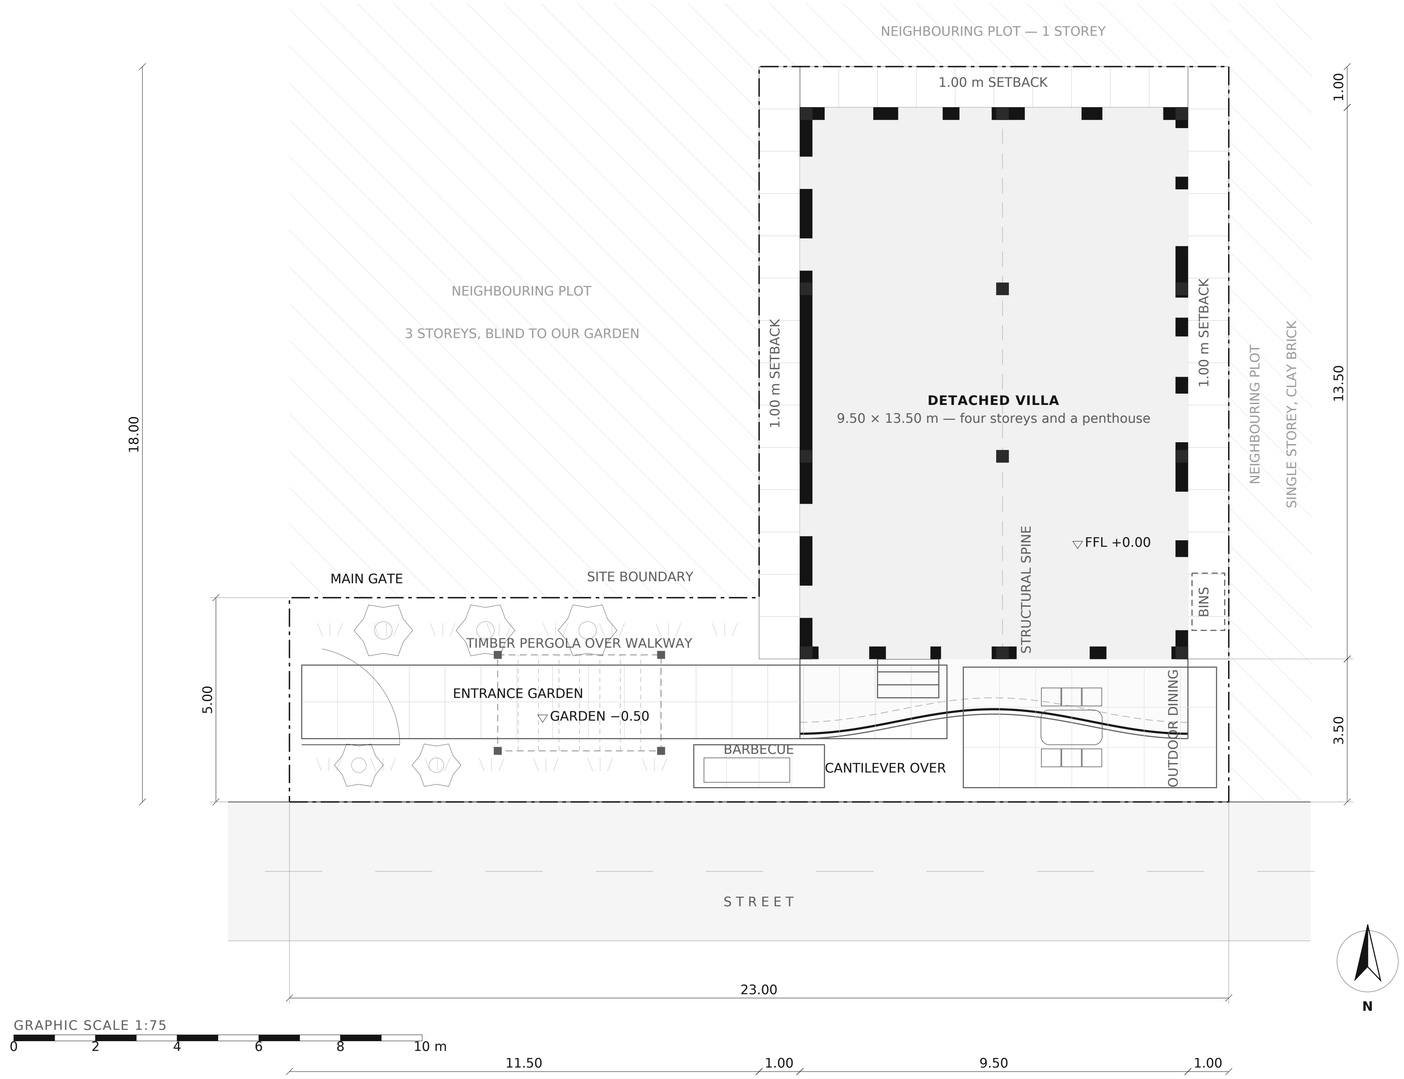

SITE PLAN — DETACHED VILLA

LEVEL +0.00 · 1:75 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

PLOT, SOUTH BAND 23.00 × 5.00	115.0 m²
PLOT, EAST PART 11.50 × 13.00	149.5 m²
TOTAL	**264.5 m²**
VILLA FOOTPRINT 9.50 × 13.50 M	128.2 m²
SITE COVERAGE	48.5 %
ENTRANCE GARDEN, WEST	57.5 m²
FORECOURT, IN FRONT	40.3 m²
SETBACKS, THREE SIDES	38.5 m²
GROSS INTERNAL AREA, FIVE STOREYS	505.2 m²

GENERAL NOTES

1. Final draft — layout agreed. The villa is detached: set back 1.00 m from the west, north and east boundaries, the three sides a neighbour stands on. The south is not set back — it faces the street across our own forecourt.

2. Footprint 9.50 × 13.50 m = 128.2 m² on a 264.5 m² plot, 48.5 % coverage against 63.0 % for the attached scheme at P4. Detaching costs 22 % of each floor and buys an open aspect on all four sides and no party wall.

3. The setbacks are our own land, so each is a 1.00 m paved side passage rather than a dead strip, reached from the forecourt on the east and from the entrance garden on the west.

4. The cantilever oversails the forecourt by 1.95 m at each end and draws in to 1.35 m at the waist, leaving at least 1.55 m clear to the street, and covers the front door and its three risers. Nothing projects over a boundary, but the overhang is subject to the local projection rule; confirm before construction.

5. The client's survey sketch recorded a 0.50 m step in the north boundary and a 5.50 m offset between the two blocks' north walls; the two cannot both be true. Resolved in favour of a straight boundary at 18.00. To be confirmed by measured survey before any work starts on site.

6. Structure is an RC frame on the grid shown, 300 mm columns on wall centrelines so none stands in a room. The A-300 enlargements are the last sheets still on the old 11.50 × 14.50 footprint.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SITE PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-000	**P19**	**1:75 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

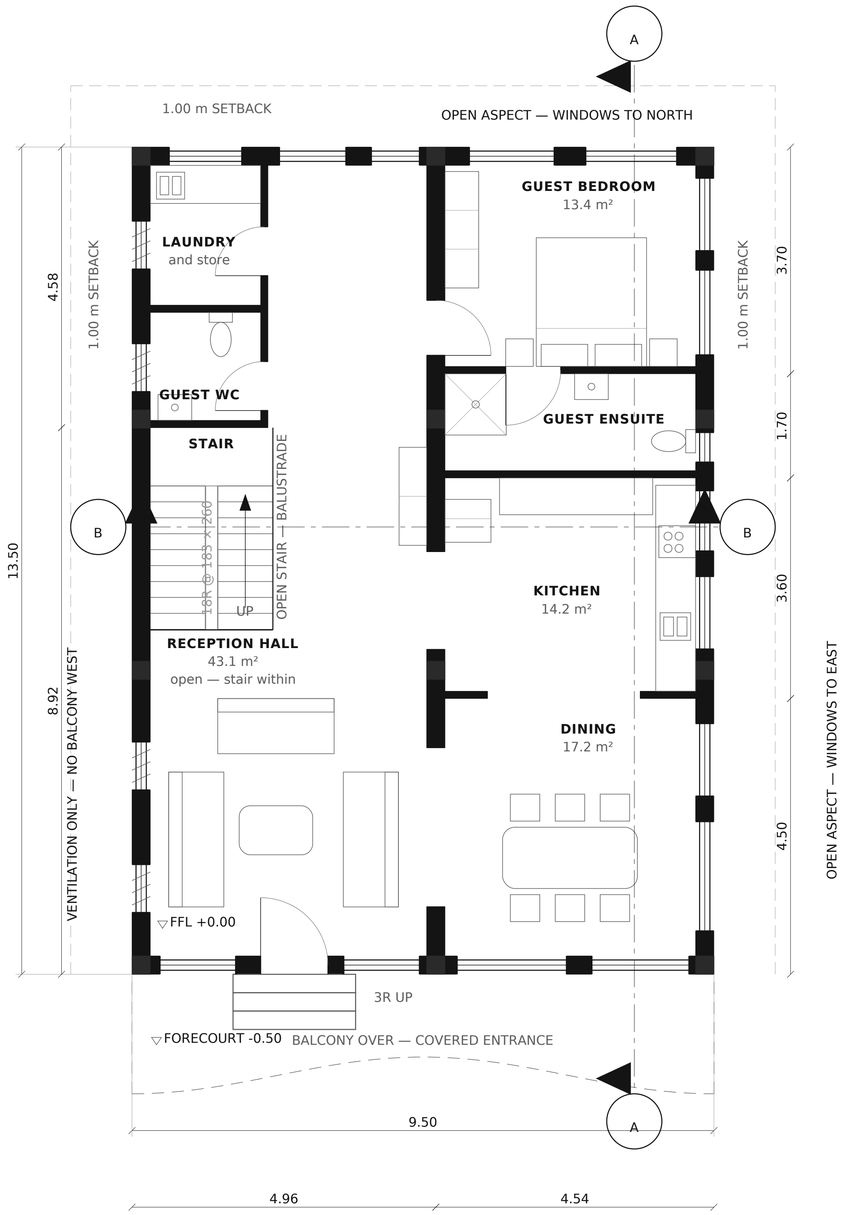

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

GROUND FLOOR PLAN — DETACHED VILLA

LEVEL +0.00 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

RECEPTION HALL	43.1 m²
STAIR	6.6 m²
GUEST WC	3.2 m²
LAUNDRY	4.1 m²
DINING	17.2 m²
KITCHEN	14.2 m²
GUEST ENSUITE	6.5 m²
GUEST BEDROOM	13.4 m²
TOTAL	**108.3 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BEDROOMS	1 — the guest suite; 8 above
FLOOR ABOVE	+3.30

GENERAL NOTES

1. Final draft — layout agreed. The floor you receive people on: the family living is upstairs where the balconies are, so this one takes arrival, eating and a guest suite for anyone who cannot manage the stair.

2. Hall, dining and kitchen are one open sequence. The spine is cased open to both at 2.60 and 1.60 m, and the kitchen serves the dining through a 2.50 m opening rather than a door. Only the guest suite and the two service rooms are closed.

3. The reception hall is the whole west strip at 43.1 m², with the stair standing in it. It turns the corner behind the stair and runs on to the north wall, so the guest bedroom opens off the hall and there is no circulation room anywhere on the floor.

4. Guest WC, laundry and store are one block against the west wall, the only part of this floor that is walled off. East and north carry ordinary windows, the west louvred ventilation only.

5. The front door is in the hall's south wall, under the cantilever, which projects about 1.75 m there — so the entrance is covered without a porch being added to the elevation. Three risers up from the forecourt at −0.50.

6. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

7. The A-300 enlargements are the last sheets still on the old 11.50 × 14.50 footprint.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


GROUND FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-100	**P19**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

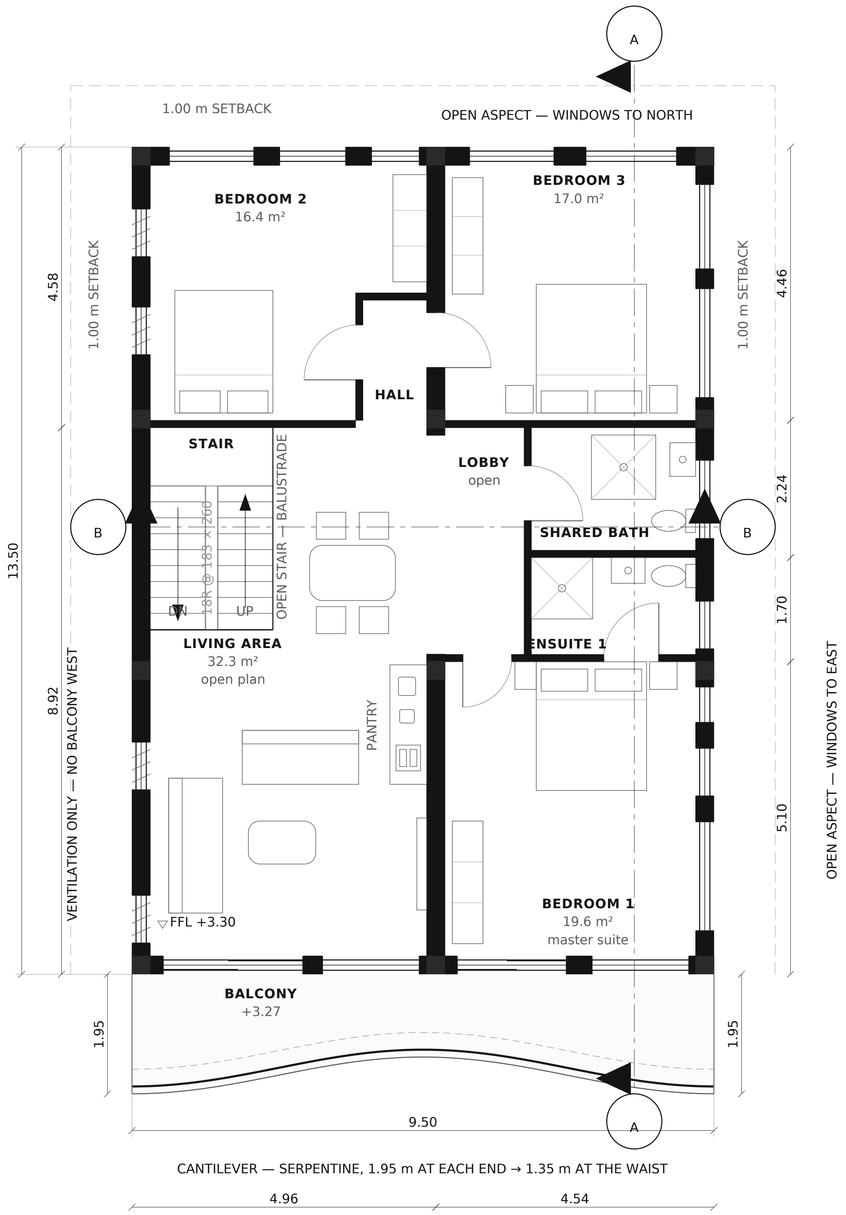





FIRST FLOOR PLAN — DETACHED VILLA

LEVEL +3.30 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

LIVING AREA	32.3 m²
STAIR	6.6 m²
BEDROOM 1 — MASTER	19.6 m²
BEDROOM 1 ENSUITE	4.2 m²
LOBBY	4.8 m²
SHARED BATH	5.4 m²
BEDROOM 2	16.4 m²
HALL	2.0 m²
BEDROOM 3	17.0 m²
TOTAL	**108.3 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BALCONY, EXTERNAL	15.7 m²
BEDROOMS	3 — the master, bedrooms 2 and 3
FLOOR ABOVE / BELOW	+6.60 / +0.00

GENERAL NOTES

1. Final draft — layout agreed. The living floor: a living area and bedrooms 1 to 3. The living area is 32.3 m² with the stair standing in it and the pantry open along the spine, opening through a sliding door onto the cantilever.

2. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

3. Bedroom 1 is the master at 19.6 m²: its north wall sits 1.30 m further north than the suite below it, and the shared bath gives up the same depth at 5.4 m².

4. The pantry is a counter against the solid stretch of spine, not the walled room the third floor has. The lobby has no wall either: the spine is opened 3.69 m between the columns, a downstand beam rather than a wall.

5. The west strip is otherwise the third floor's and the east strip the second's, so the wet rooms stack and the stair lines through. East and north carry ordinary windows, the west louvred ventilation only. The hall to the north bedrooms stops at its last door; the dead end beyond goes to bedroom 2, 16.4 m².

6. The cantilever runs on all three upper floors and the penthouse — the same serpentine, 1.95 m deep at each end drawing in to 1.35 m at the waist, 15.7 m² — with sliding doors from the living area and bedroom 1.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

FIRST FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-101	**P19**	**1:50 @ A1**	**2026-10-07**


Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

SECOND FLOOR PLAN — DETACHED VILLA

LEVEL +6.60 · 1:50 @ A1 · METRES

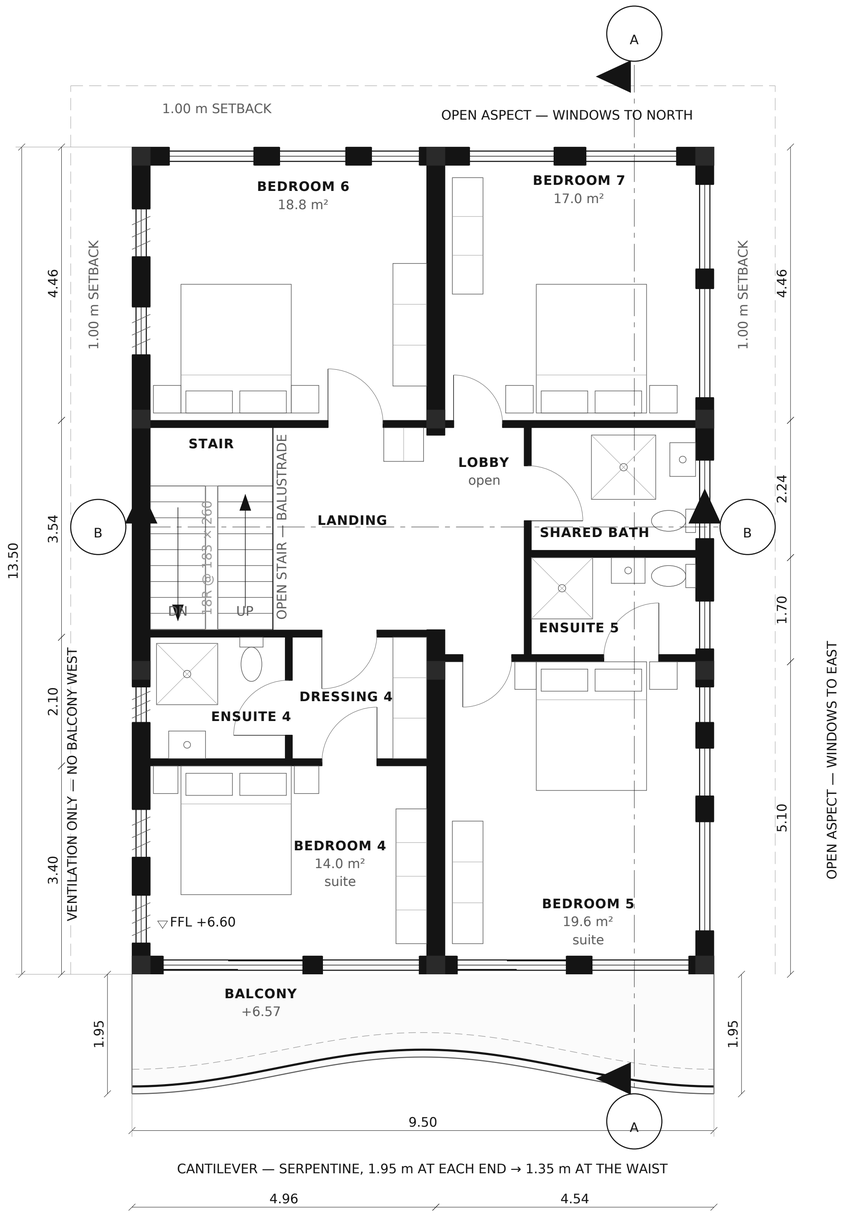





KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

BEDROOM 4 — SUITE	14.0 m²
BEDROOM 4 ENSUITE	4.4 m²
BEDROOM 4 DRESSING	4.3 m²
BEDROOM 5 — SUITE	19.6 m²
BEDROOM 5 ENSUITE	4.2 m²
LOBBY	4.8 m²
STAIR	6.6 m²
LANDING	7.9 m²
SHARED BATH	5.4 m²
BEDROOM 6	18.8 m²
BEDROOM 7	17.0 m²
TOTAL	**107.0 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BALCONY, EXTERNAL	15.7 m²
BEDROOMS	4 — two of them suites
FLOOR ABOVE / BELOW	+9.90 / +3.30

GENERAL NOTES

1. Final draft — layout agreed. A bedroom floor: bedrooms 4 to 7, two of them suites, on the detached envelope.

2. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

3. Bedroom 4 takes the south-west with its ensuite and dressing behind; bedroom 5 the south-east, its ensuite off the bedroom.

4. The east strip is the first floor's, line for line — shared bath 5.4 m², lobby 4.8 m², bedroom 5 at 19.6 m² as its wall moves 1.30 m north. Every wet room and east window stacks, one drainage stack each, straight to the ground.

5. The lobby has no door: the spine is opened its whole length between the columns, so lobby and landing read as one space. It serves bedroom 5, the shared bath and bedroom 7. Bedroom 6 has the old hall — the whole north-west quarter, 18.8 m².

6. The cantilever is carried here too — the same serpentine, 1.95 m at each end, 1.35 m at the waist, 15.7 m². Both suites open onto it; a screen between them is worth considering.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

SECOND FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-102	**P19**	**1:50 @ A1**	**2026-10-07**


Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

THIRD FLOOR PLAN — DETACHED VILLA

LEVEL +9.90 · 1:50 @ A1 · METRES

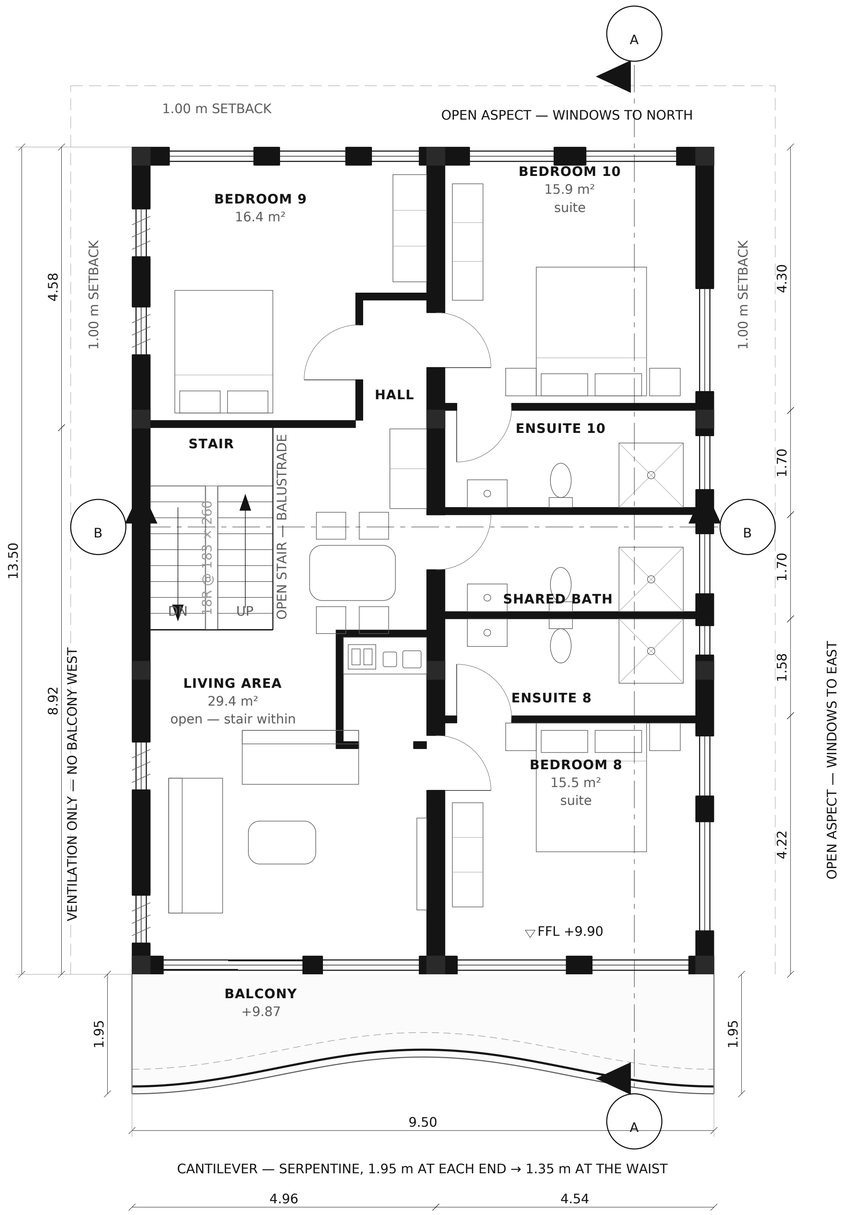





KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

AREA SCHEDULE

LIVING AREA	29.4 m²
STAIR	6.6 m²
HALL	2.0 m²
BEDROOM 8 — SUITE	15.5 m²
BEDROOM 8 ENSUITE	6.5 m²
SHARED BATH	6.5 m²
BEDROOM 10 ENSUITE	6.5 m²
BEDROOM 10 — SUITE	15.9 m²
BEDROOM 9	16.4 m²
TOTAL	**105.3 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BALCONY, EXTERNAL	15.7 m²
ROOF OVER, TOP OF SLAB	+13.20

GENERAL NOTES

1. Final draft — layout agreed. The building is set back 1.00 m from the west, north and east boundaries; the south faces the street across our own forecourt. Detaching costs 22% of the floor — 114.8 m² against 147.3 — and removes the party wall, so one structural spine divides the plate.

2. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

3. The west strip south of bedroom 9 is one room: no wall divides the living area from the stair standing in it. The stair is a private villa stair — 900 mm flights, 18R at 183 × 260 — needing no enclosure, no smoke vent and no lift.

4. The south cantilever is reinforced concrete: a serpentine of one full period, 1.95 m deep at both ends and drawn in to 1.35 m at the waist, which is deep enough to sit out on along the whole frontage.

5. East and north carry ordinary windows. The east neighbour is a single storey in clay brick 1.00 m away, so they clear its roof by 1.20 m at the first floor. The west is louvred only — that neighbour is 3 storeys, and blind toward us.

6. Bedroom 8 and the shared bath open off the living area; bedrooms 9 and 10 off the hall, whose dead end goes to bedroom 9. Bedroom 10 has no balcony: it takes the north wall and two windows.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


THIRD FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-103	**P19**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

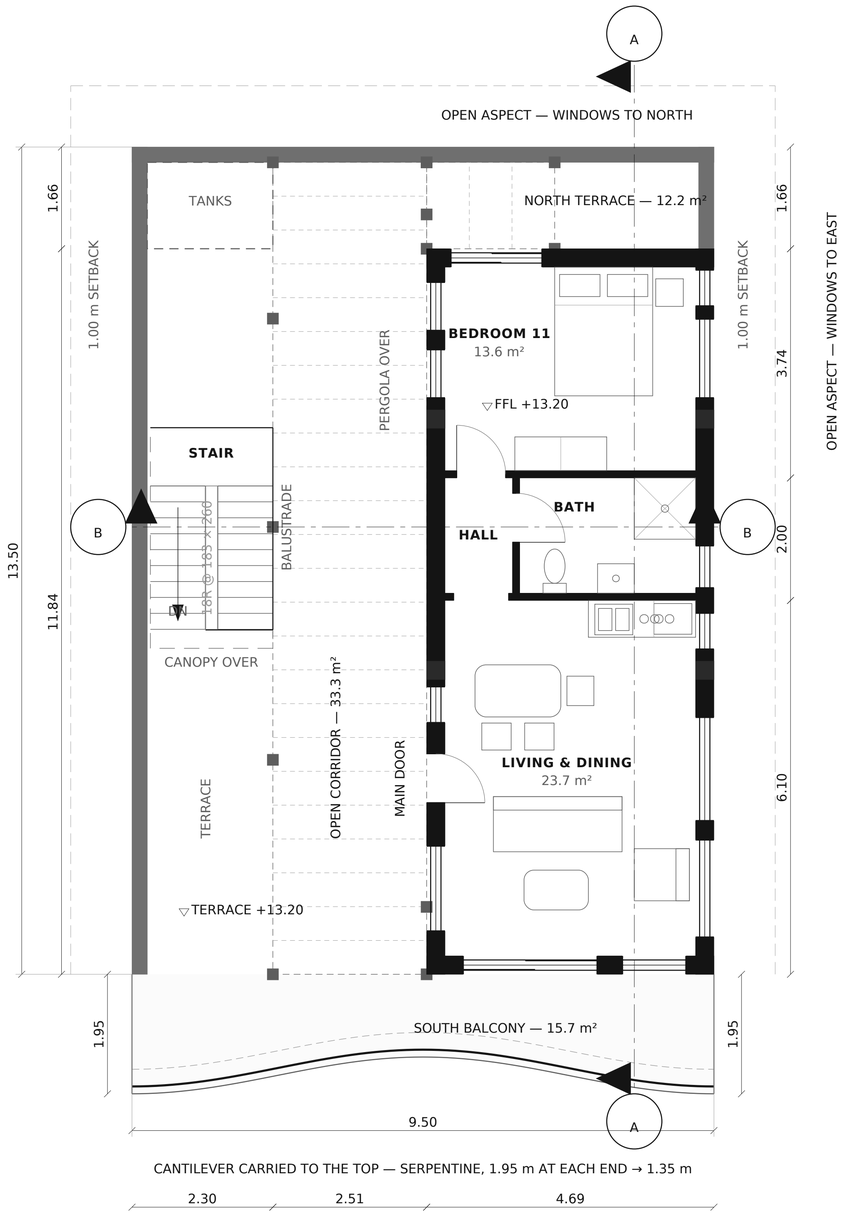

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

PENTHOUSE PLAN — DETACHED VILLA

LEVEL +13.20 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

AREA SCHEDULE

LIVING AND DINING	23.7 m²
HALL	2.1 m²
BATH	5.4 m²
BEDROOM 11	13.6 m²
TOTAL	**44.8 m²**
GROSS INTERNAL AREA, FLAT	46.0 m²
SOUTH BALCONY, ON THE CANTILEVER	15.7 m²
SOUTH TERRACE, WEST OF THE CORRIDOR	11.5 m²
NORTH TERRACE	12.2 m²
OPEN CORRIDOR	33.3 m²
TOP OF PENTHOUSE SLAB	+16.45
FLOOR BELOW	+9.90

GENERAL NOTES

1. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number. This is bedroom 11.

2. Final draft — layout agreed. The two open areas are joined outside the flat, down the west, by a corridor 2.51 m clear against the 2.00 m asked for, pergola over its whole length. The front door is off it.

3. 46.0 m² indoors; 15.7 m² of balcony on the cantilever, 11.5 m² of terrace by the stair, 12.2 m² north and 33.3 m² of corridor — all four run into one another.

4. The corridor passes east of the stair: the well is 2.00 m wide and hard against the west parapet, its half landing 1.65 m below this floor, so it stays open. Its east side is the flat's west wall, on the spine at x 17.46 — the one line on this side of the roof with a beam under it.

5. That leaves the flat 4.09 m clear, which will not take two bedrooms side by side: stacking them needs 12.06 m of the 13.50 m depth and leaves 1.44 m for both terraces. The second bedroom is what pays for the corridor.

6. The living room runs south to the building's face, so it opens straight onto the cantilever; y 3.65 is a grid line, so that wall sits on the columns and over the wall below. At +16.45 the penthouse is a fourth storey for most planning codes.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

PENTHOUSE PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-104	**P19**	**1:50 @ A1**	**2026-10-07**


Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

ROOF PLAN

LEVEL +16.45 / +13.20 · 1:50 @ A1 · METRES

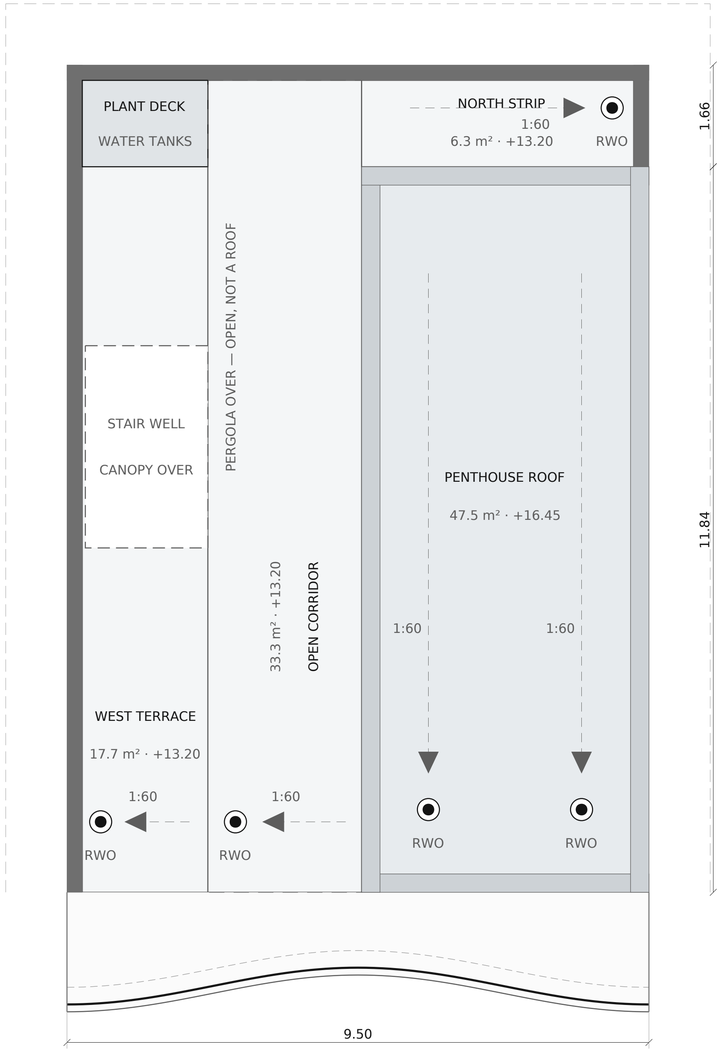

BALCONY +13.20 — 15.7 m², FALLS TO THE EDGE

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

THE ROOF

ROOF OVER PENTHOUSE	+16.45
TERRACES AND BALCONY	+13.20
PARAPET	250 mm × 1100 high
WATERPROOFING UPSTAND	150 mm minimum
FALLS	1:60, indicative
OUTLETS	5, indicative — see PL-200
BALCONY	15.7 m², falls to the edge
PLANT DECK	water tanks, north-west

GENERAL NOTES

1. The surfaces that shed water, which no other sheet draws: the roof over the penthouse at +16.45, the terraces and the open corridor at +13.20, the balcony, and the plant deck.

2. Outlines, parapets, the plant deck and the levels are measured from the geometry and are exact. The falls and the outlet positions are architectural intent, drawn so the drainage package has something to coordinate against.

3. PL-200 and PL-300 set the outlet positions, the pipe sizes, the downpipe routes and the overflow provision. Nothing here is a drainage design.

4. Waterproofing turned up 150 mm minimum at every parapet, upstand and threshold and dressed into the outlet. Membrane and insulation build-up to the specification.

5. The pergola over the corridor is open and is not a roof: the corridor under it is an external surface and drains as one. The stair well is open to the sky under its canopy.

6. The areas here are drainage zones, not the use areas on A-104, and they divide the same surfaces differently — hence "north strip" rather than A-104's north terrace, which also counts the slab north of the stair. The two differ by 0.17 m²: A-104 deducts the full 2.05 m strip for the stair well, which is 2.00 m wide.

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


ROOF PLAN

DRAWING No	REVISION	SCALE	DATE
ARC-106	**P19**	**1:50 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

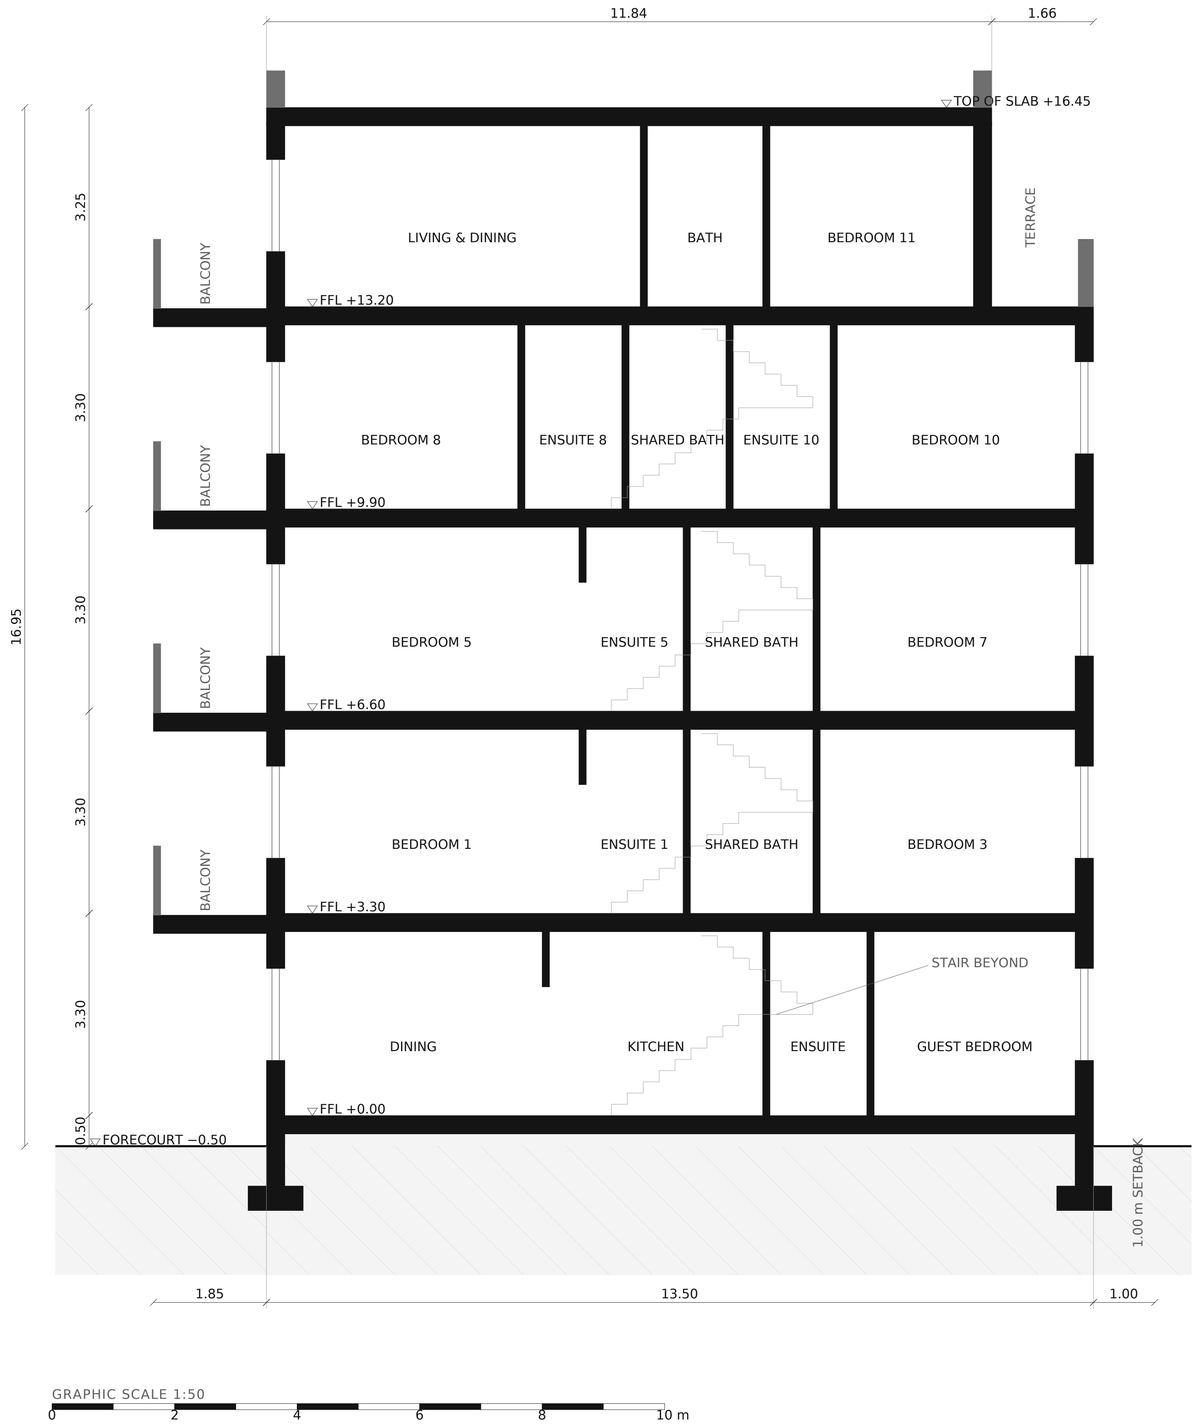

SECTION A–A — DETACHED VILLA

LEVEL looking west · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

LEVEL DATUMS

FORECOURT AND GARDEN	-0.50
GROUND FLOOR	+0.00
FIRST FLOOR	+3.30
SECOND FLOOR	+6.60
THIRD FLOOR	+9.90
PENTHOUSE FLOOR	+13.20
PENTHOUSE, TOP OF SLAB	+16.45
CLEAR CEILING HEIGHT	3.00 m
STRUCTURAL ZONE	0.30 m
OVERALL, GARDEN TO TOP	16.95 m

GENERAL NOTES

1. Final draft — layout agreed. Looking west, cut on the line marked A–A on every plan, at x 20.70. That line is not arbitrary: it is the one north-south cut that passes through a room at every level and through every wet room in the east strip, and it clears all three column lines, so the slabs are seen spanning rather than a column standing in the cut.

2. The wet rooms on the first and second floors sit one over the other, wall for wall — 8.60, 10.30 and 12.42 on both — so each drops a single drainage stack straight to the ground. The third floor divides the strip on its own lines and is shown as it is.

3. Flat slab on the column grid, 300 mm structural zone, giving 3.00 m clear at every level and 3.30 m floor to floor; the penthouse is 3.25 m floor to top of slab.

4. The south cantilever is carried on all three upper floors and the penthouse. It projects 1.85 m at this cut, against 1.95 m at each end of the curve and 1.35 m at its waist, with a glass balustrade at the slab edge.

5. The penthouse stands clear of the north edge, leaving the roof terrace beyond its north wall. The corridor that joins the two terraces runs west of this cut and does not appear; see A-104.

6. The stair is drawn in thin line beyond the cut, where it is seen through the open spine. Foundations are indicative only and subject to a ground investigation and the engineer's design.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SECTION A–A — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-200	**P19**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

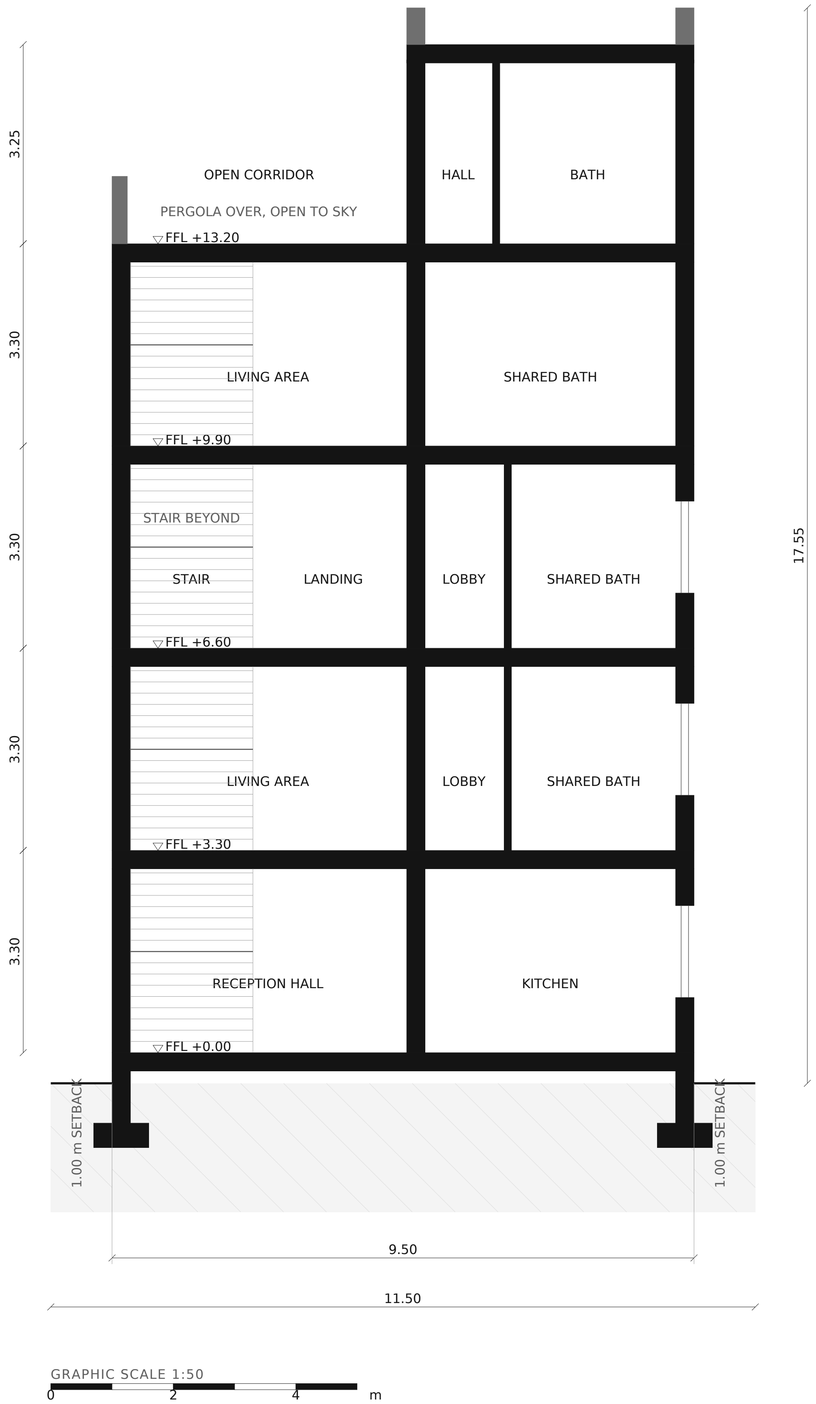

SECTION B–B — TRANSVERSE

LEVEL looking north · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

THE CUT

SECTION LINE	y = 10.80, looking north
WIDTH BETWEEN SETBACKS	9.50 m
STRUCTURAL SPINE	x 17.31 – 17.61
FLOOR TO FLOOR	3.30 m
CLEAR HEIGHT	3.00 m
STRUCTURAL ZONE	300 mm
TOP OF BUILDING	+17.05
EAST GLAZED AT THIS CUT	levels 0, 1 and 2

GENERAL NOTES

1. Cut at y = 10.80, inside the stair well and clear of every cross wall, looking north. A-A cuts the other way and shows the depth; this is the only drawing of the width.

2. What the cut passes through was read off the plans by the probe in checks.py, not written from memory, and whether the east wall is glazed at the cut is worked out from the plan's own opening list each time the sheet is built.

3. The east wall is glazed on the lower three floors and solid on the third, which is the plans' arrangement and not a drafting choice. It can be glazed at all because the neighbour a metre east is a single storey.

4. The stair is beyond the cut, not in it: its flights run north-south, so this section crosses them end-on and they are drawn in thin line as seen through the open well.

5. At the penthouse the west half of the plate is the open corridor, outside the flat and open to the sky under its pergola. Foundations are indicative pending GEO-001.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

SECTION B–B — TRANSVERSE

DRAWING No	REVISION	SCALE	DATE
ARC-301	**P19**	**1:50 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor



THE BALCONY CURVE IN PLAN — IT CANNOT SHOW IN ELEVATION

1.95 m DEEPEST · 1.35 m SHALLOWEST · 15.7 m² A FLOOR



GRAPHIC SCALE 1:100

0 2 4 m

SOUTH ELEVATION — SCHEME A “WAVE”

LEVEL street frontage · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

SCHEME A — WAVE

WALLS	warm limestone render
SLAB NOSING	rounded, 180 mm
COVE LIGHT	in the underside of the nosing
BALUSTRADE	clear glass, 120 mm inboard
FRAMES	bronze anodised
BALCONY CURVE	serpentine
PROJECTION	1.95 / 1.35 m
BALCONY AREA	15.7 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. The exterior only. The plans, site plan and section are agreed and re-issued to the adopted curve; nothing here changes the rest of them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. Scheme A takes its material from the contemporary reference: warm limestone render, a rounded slab nosing with a cove light tucked into its underside, clear glass balustrades and planting along the balcony edge. The four south bays read as glazed ribbons between the slabs.

4. The balcony curve is a serpentine — one full period across the frontage, 1.95 m deep at each end drawn in to 1.35 m at the waist. At 1.35 m is usable the whole way along; the deep ends carry the dining and the furniture.

5. This is the adopted curve, and the plans are drawn to it. It cost area to take: 15.7 m² a floor against the 17.4 m² of the curve it replaced, 7 m² over the four balcony levels. A-000 and A-100 to A-104 are re-issued to it.

6. The balconies do not wrap the corner as the reference does: the 1.00 m setbacks forbid anything projecting west, north or east, so the cantilever stays on the street frontage.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

SOUTH ELEVATION — SCHEME A “WAVE”

DRAWING No	REVISION	SCALE	DATE
A-400	**P19**	**1:50 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor



SIDE & REAR ELEVATIONS — SCHEME A “WAVE”

LEVEL east, north and west · 1:75 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

SCHEME A — WAVE

WALLS	warm limestone render
SLAB NOSING	rounded, 180 mm
COVE LIGHT	in the underside of the nosing
BALUSTRADE	clear glass, 120 mm inboard
FRAMES	bronze anodised
BALCONY CURVE	serpentine
PROJECTION	1.95 / 1.35 m
BALCONY AREA	15.7 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. The exterior only. The plans, site plan and section are agreed and re-issued to the adopted curve; nothing here changes the rest of them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. The east and north boundaries are open and carry ordinary windows on every floor. The west is the blind elevation: louvred ventilation only, drawn at high level, and nothing projects.

4. The penthouse stands back 4.81 m from the west and 1.66 m from the north, so on those two faces it is drawn in thin line behind the roof terrace parapet.

5. The balcony appears on the street frontage only and so does not show on any of these three faces.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SIDE & REAR ELEVATIONS — SCHEME A “WAVE”

DRAWING No	REVISION	SCALE	DATE
A-401	**P19**	**1:75 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

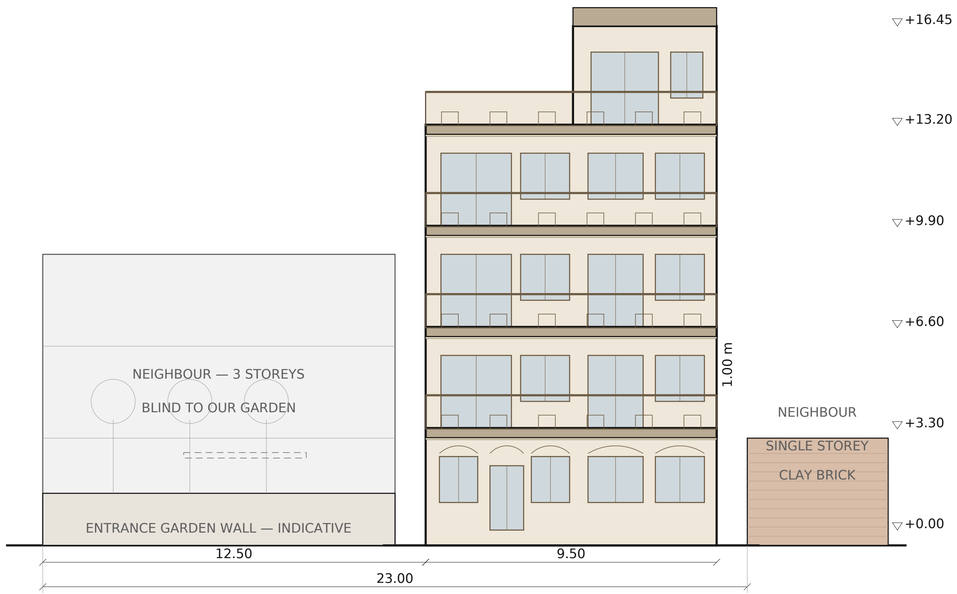

SCHEME A — WAVE, ADOPTED

STREET ELEVATION IN CONTEXT

LEVEL scheme A, as surveyed · 1:100 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AS SURVEYED

PLOT WIDTH	23.00 m
ENTRANCE GARDEN, WEST	11.50 m
VILLA FRONTAGE	9.50 m
SIDE PASSAGE, EAST	1.00 m
WEST NEIGHBOUR	3 storeys, blind
EAST NEIGHBOUR	1 storey, clay brick
NORTH NEIGHBOUR	1 storey
OUR TOP OF BUILDING	+17.05
WE STAND OVER THE EAST	14.05 m

GENERAL NOTES

1. Preliminary — the exterior only, and the first drawing in the set to show the villa against the houses it actually stands between.

2. The house is not in the middle of its plot. It sits hard against the east boundary with a 1.00 m paved side passage, and the whole 11.50 m entrance garden is on the west, gated from the west boundary with a walk running east to the front door.

3. East: a single storey in clay brick, 1.00 m away. That is what lets the east wall be glazed at all — our lowest east sill at +4.20 clears its roof by 1.20 m. We stand 14.05 m over it, which is worth seeing before the elevations are agreed.

4. West: 3 storeys and blind toward us, drawn in thin line because it stands back behind the garden. Nothing of ours opens that way in any case — the west wall takes louvred ventilation only.

5. North: a single storey as well, confirmed by the client and not drawn on this south-facing view. The north wall carries windows on all five levels; only the ground floor looks at anything, and from +3.30 up they clear its roof as the east windows clear the east neighbour's.

6. The garden wall height is indicative and awaits the client's choice. Boundaries to be confirmed by measured survey.

GRAPHIC SCALE 1:100

0 2 4 6 8 10 m

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


STREET ELEVATION IN CONTEXT

DRAWING No	REVISION	SCALE	DATE
A-402	**P19**	**1:100 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS


P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

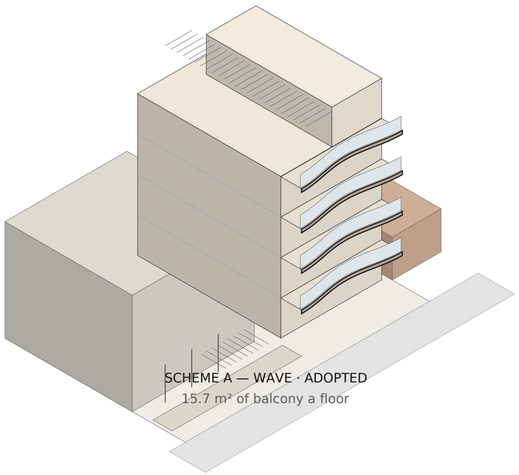

SCHEME A — WAVE · ADOPTED
15.7 m² of balcony a floor

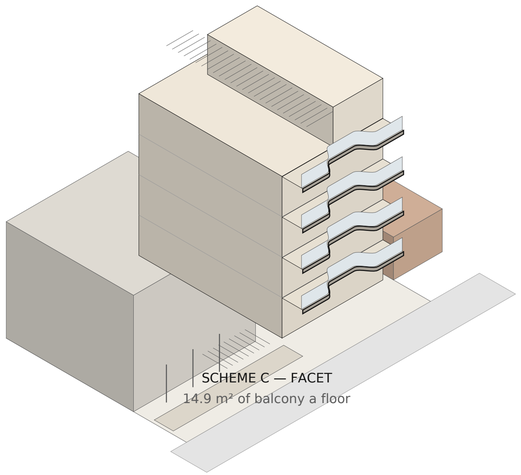

SCHEME C — FACET
14.9 m² of balcony a floor

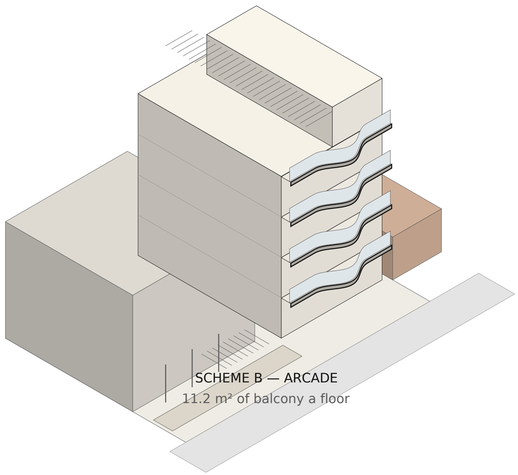

SCHEME B — ARCADE
11.2 m² of balcony a floor

AXONOMETRIC — THREE BALCONY OPTIONS

LEVEL from the south-west · 1:250 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

THE FOUR CURVES OFFERED

A — SERPENTINE, ADOPTED	15.7 m² a floor
C — FACET	14.9 m² a floor
B — BOWED CENTRE BAY	11.2 m² a floor
SUPERSEDED CURVE	17.4 m² a floor
DEEPEST ALLOWED	2.00 m
SHALLOWEST USABLE	0.60 m
WEST NEIGHBOUR	3 storeys, blind
EAST NEIGHBOUR	1 storey, clay brick

GENERAL NOTES

1. Preliminary. Isometric from the south-west, which is the one corner that shows the street frontage, the blind west wall, the roof pergola and the entrance garden at once.

2. This is a projection, not a render: every line is a transform of the constants the plans are drawn from, so it cannot show a balcony, a garden or a neighbour that the drawings do not have.

3. All three sit on the real plot. The villa is hard against the east boundary with a 1.00 m side passage and the 11.50 m entrance garden on the west, the three-storey blind neighbour standing back behind it and the single-storey clay-brick one a metre to the east.

4. Scheme A is the one adopted, and the plans are drawn to its curve. B and C are kept here as the record of what was offered; their elevation sheets are stamped not selected and are not bound into the issue.

5. The balconies stop at the corner on all three: the 1.00 m setbacks forbid anything projecting west, north or east.

6. Faces are painted back to front rather than depth-sorted, so a detail may overlap where two surfaces nearly touch. The measured elevations A-400 and A-401 govern.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

AXONOMETRIC — THREE BALCONY OPTIONS

DRAWING No	REVISION	SCALE	DATE
A-430	**P19**	**1:250 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

DOOR & WINDOW SCHEDULE

95 OPENINGS · 24 TYPES · MEASURED FROM THE PLANS

MARK	1:100	W × H mm	SILL	FACE	L0	L1	L2	L3	L4	No.
D01 Door		2300 × 2400	floor	S	·	1	1	1	·	**3**
D02 Door		2200 × 2400	floor	S	·	·	·	·	1	**1**
D03 Door		1800 × 2400	floor	S	·	1	1	·	·	**2**
D04 Door		1500 × 2400	floor	N	·	·	·	·	1	**1**
D05 Door		1100 × 2100	floor	S	1	·	·	·	·	**1**
D06 Door		800 × 2400	floor	W	·	·	·	·	1	**1**
W01 Window		1800 × 1500	+900	SE	2	2	2	2	·	**8**
W02 Window		1700 × 1500	+900	E	·	·	·	1	1	**2**
W03 Window		1600 × 1500	+900	SE	1	2	2	2	1	**8**
W04 Window		1500 × 1500	+900	N	1	1	1	1	·	**4**
W05 Window		1400 × 1500	+900	ENW	2	3	3	2	1	**11**
W06 Window		1300 × 1500	+900	E	·	1	1	·	1	**3**
W07 Window		1250 × 1500	+900	S	2	·	·	·	·	**2**
W08 Window		1200 × 1500	+900	EN	4	·	·	·	·	**4**
W09 Window		1100 × 1500	+900	N	1	1	1	1	·	**4**
W10 Window		1050 × 1500	+900	S	·	·	·	·	1	**1**
W11 Window		1000 × 1500	+900	E	1	·	·	2	·	**3**
W12 Window		900 × 1500	+900	E	·	·	·	1	·	**1**
W13 Window		800 × 1500	+900	ENW	1	3	3	1	2	**10**
W14 Window		700 × 1500	+900	E	·	·	·	·	1	**1**
W15 Window		600 × 1500	+900	EW	·	1	1	·	3	**5**
W16 Window		500 × 1500	+900	E	1	·	·	1	·	**2**
L01 Louvre		800 × 500	+2100	W	4	4	4	4	·	**16**
L02 Louvre		600 × 500	+2100	W	·	·	1	·	·	**1**

DOOR & WINDOW SCHEDULE

SCHEDULE · ALL FIVE LEVELS · MILLIMETRES

THE OPENINGS

DOORS	9
WINDOWS	69
LOUVRES	17
TYPES	24
DOOR AREA	38.3 m²
GLAZED AREA	127.9 m²
LOUVRE AREA	6.7 m²
WINDOW HEAD, EVERY LEVEL	+2.40 above floor
WINDOW SILL, EVERY LEVEL	+0.90 above floor

GENERAL NOTES

1. Measured from the plans, not compiled beside them. Every opening is a pair of coordinates the plan cuts its wall with and the elevation draws its frame in, so this schedule and those drawings cannot disagree about a width.

2. Marks run largest first within each kind, so D01 is the widest door and W01 the widest window. L marks are the west wall's louvres: that face is blind below the penthouse and ventilates only.

3. Heads and sills are constant through the building — sill +0.90, head +2.40 — so a type is distinguished by its width alone except at the doors.

4. Operation, frame material, glazing specification, ironmongery and finishes are not set by the geometry and are not invented here. They belong to ARC-600 and the specification.

5. Dimensions are structural opening sizes. Frame and tolerance allowances to be taken off by the supplier against the construction drawings.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

DOOR & WINDOW SCHEDULE

DRAWING No	REVISION	SCALE	DATE
ARC-500	**P19**	**1:100 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

REFLECTED CEILING PLAN — GROUND FLOOR

LEVEL +0.00 · 1:50 @ A1 · METRES

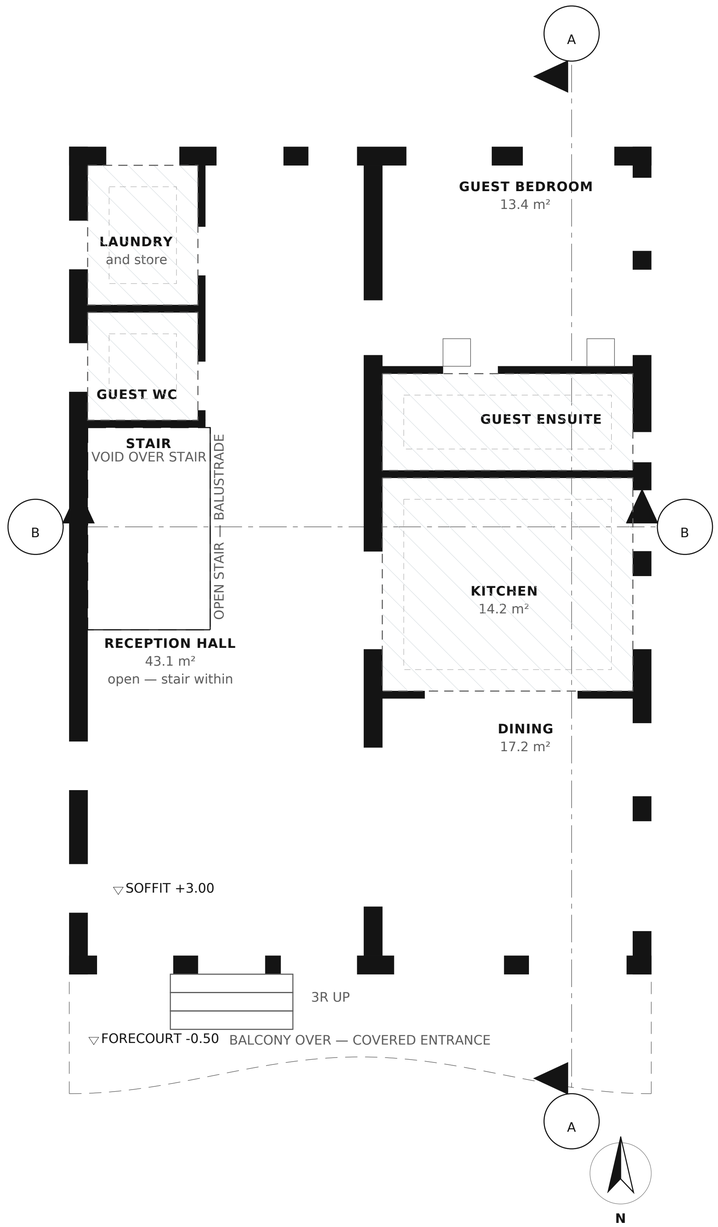

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

THE CEILING

FINISHED FLOOR LEVEL	+0.00
SOFFIT, GENERALLY	+3.00
CLEAR HEIGHT	3.00 m
STRUCTURAL ZONE OVER	300 mm
FLOOR TO FLOOR	3.30 m
BULKHEADS SHOWN	4 wet rooms
BULKHEAD DEPTH	by the services engineer
LIGHT FITTINGS	see EL-200 series

GENERAL NOTES

1. The ceiling of the ground floor, seen from below. Drawn by running the floor plan with its sanitaryware, furniture, door swings and dimension chains switched off, so it cannot stop agreeing with A-100 when a partition moves.

2. Soffit is +3.00 throughout, 3.00 m clear, under a 300 mm structural zone. Any local drop below that is a bulkhead and is shown as one.

3. A bulkhead is drawn over every room the plan calls wet, because that is where the drainage runs. The outline is the room; the depth, the exact extent and everything inside it are the services engineer's and are set on the ME and PL series.

4. No light fitting is drawn. Fittings, switching and emergency provision are the EL-200 series; a layout invented here would only have to be thrown away.

5. Ceiling finishes, board type, moisture resistance in the wet rooms and access panels are specification, not geometry, and are not set on this sheet.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


REFLECTED CEILING PLAN — GROUND FLOOR

DRAWING No	REVISION	SCALE	DATE
ARC-400	**P19**	**1:50 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

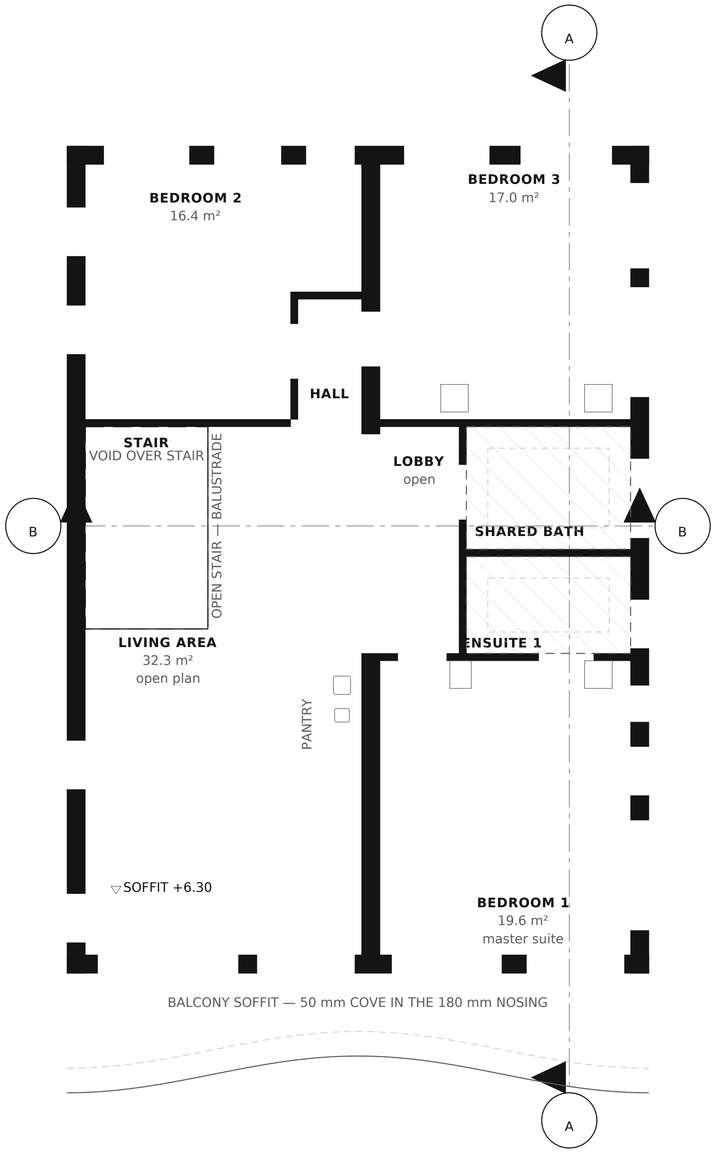

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

REFLECTED CEILING PLAN — FIRST FLOOR

LEVEL +3.30 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

THE CEILING

FINISHED FLOOR LEVEL	+3.30
SOFFIT, GENERALLY	+6.30
CLEAR HEIGHT	3.00 m
STRUCTURAL ZONE OVER	300 mm
FLOOR TO FLOOR	3.30 m
BULKHEADS SHOWN	2 wet rooms
BULKHEAD DEPTH	by the services engineer
LIGHT FITTINGS	see EL-200 series

GENERAL NOTES

1. The ceiling of the first floor, seen from below. Drawn by running the floor plan with its sanitaryware, furniture, door swings and dimension chains switched off, so it cannot stop agreeing with A-101 when a partition moves.

2. Soffit is +6.30 throughout, 3.00 m clear, under a 300 mm structural zone. Any local drop below that is a bulkhead and is shown as one.

3. A bulkhead is drawn over every room the plan calls wet, because that is where the drainage runs. The outline is the room; the depth, the exact extent and everything inside it are the services engineer's and are set on the ME and PL series.

4. No light fitting is drawn. Fittings, switching and emergency provision are the EL-200 series; a layout invented here would only have to be thrown away.

5. Ceiling finishes, board type, moisture resistance in the wet rooms and access panels are specification, not geometry, and are not set on this sheet.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

REFLECTED CEILING PLAN — FIRST FLOOR

DRAWING No	REVISION	SCALE	DATE
ARC-401	**P19**	**1:50 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

REFLECTED CEILING PLAN — SECOND FLOOR

LEVEL +6.60 · 1:50 @ A1 · METRES

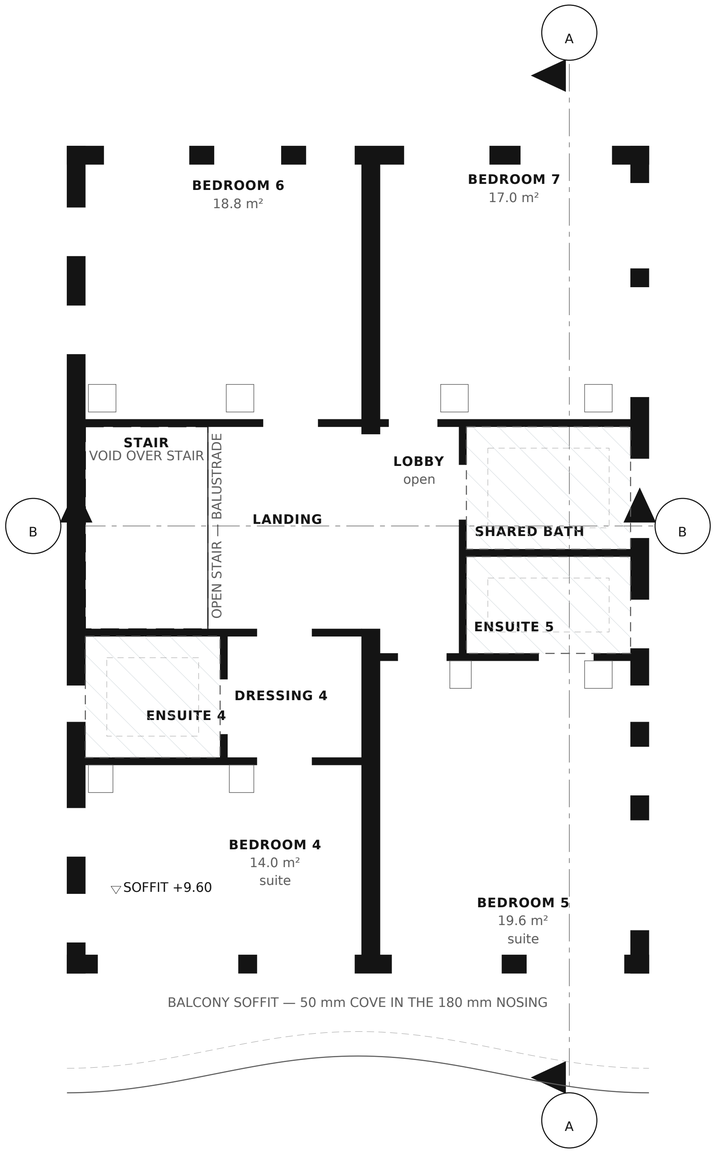

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

THE CEILING

FINISHED FLOOR LEVEL	+6.60
SOFFIT, GENERALLY	+9.60
CLEAR HEIGHT	3.00 m
STRUCTURAL ZONE OVER	300 mm
FLOOR TO FLOOR	3.30 m
BULKHEADS SHOWN	3 wet rooms
BULKHEAD DEPTH	by the services engineer
LIGHT FITTINGS	see EL-200 series

GENERAL NOTES

1. The ceiling of the second floor, seen from below. Drawn by running the floor plan with its sanitaryware, furniture, door swings and dimension chains switched off, so it cannot stop agreeing with A-102 when a partition moves.

2. Soffit is +9.60 throughout, 3.00 m clear, under a 300 mm structural zone. Any local drop below that is a bulkhead and is shown as one.

3. A bulkhead is drawn over every room the plan calls wet, because that is where the drainage runs. The outline is the room; the depth, the exact extent and everything inside it are the services engineer's and are set on the ME and PL series.

4. No light fitting is drawn. Fittings, switching and emergency provision are the EL-200 series; a layout invented here would only have to be thrown away.

5. Ceiling finishes, board type, moisture resistance in the wet rooms and access panels are specification, not geometry, and are not set on this sheet.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

REFLECTED CEILING PLAN — SECOND FLOOR

DRAWING No	REVISION	SCALE	DATE
ARC-402	**P19**	**1:50 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

REFLECTED CEILING PLAN — THIRD FLOOR

LEVEL +9.90 · 1:50 @ A1 · METRES

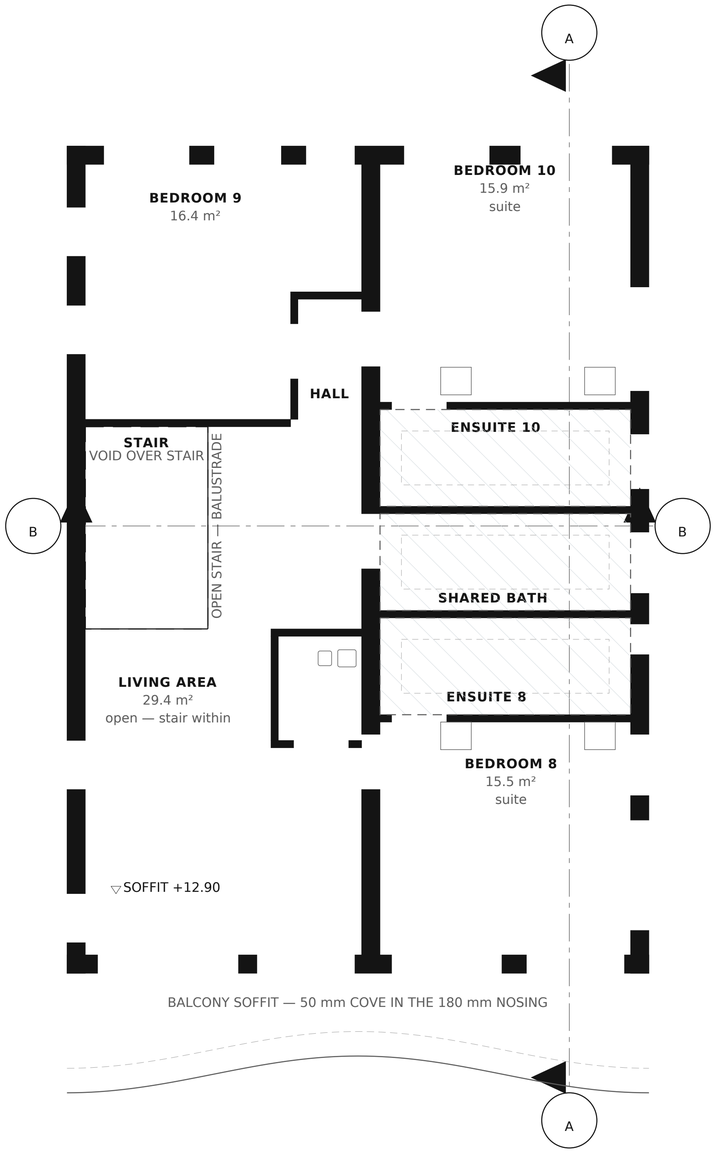

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

THE CEILING

FINISHED FLOOR LEVEL	+9.90
SOFFIT, GENERALLY	+12.90
CLEAR HEIGHT	3.00 m
STRUCTURAL ZONE OVER	300 mm
FLOOR TO FLOOR	3.30 m
BULKHEADS SHOWN	3 wet rooms
BULKHEAD DEPTH	by the services engineer
LIGHT FITTINGS	see EL-200 series

GENERAL NOTES

1. The ceiling of the third floor, seen from below. Drawn by running the floor plan with its sanitaryware, furniture, door swings and dimension chains switched off, so it cannot stop agreeing with A-103 when a partition moves.

2. Soffit is +12.90 throughout, 3.00 m clear, under a 300 mm structural zone. Any local drop below that is a bulkhead and is shown as one.

3. A bulkhead is drawn over every room the plan calls wet, because that is where the drainage runs. The outline is the room; the depth, the exact extent and everything inside it are the services engineer's and are set on the ME and PL series.

4. No light fitting is drawn. Fittings, switching and emergency provision are the EL-200 series; a layout invented here would only have to be thrown away.

5. Ceiling finishes, board type, moisture resistance in the wet rooms and access panels are specification, not geometry, and are not set on this sheet.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


REFLECTED CEILING PLAN — THIRD FLOOR

DRAWING No	REVISION	SCALE	DATE
ARC-403	**P19**	**1:50 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

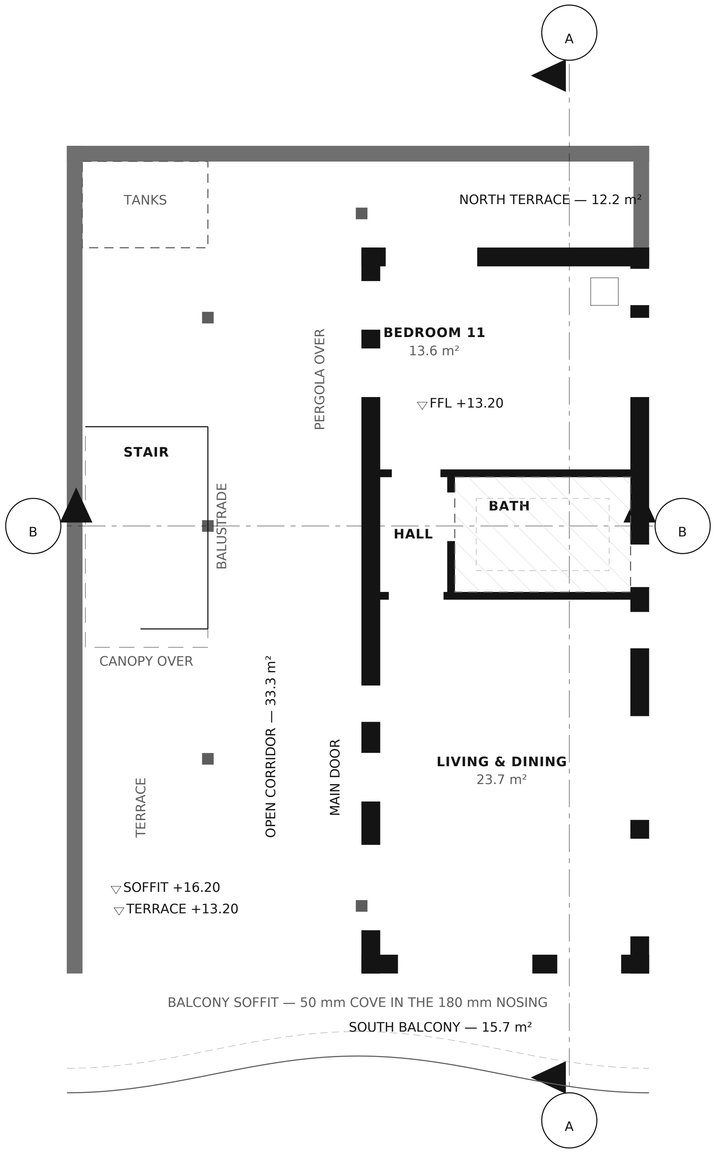

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

REFLECTED CEILING PLAN — PENTHOUSE FLOOR

LEVEL +13.20 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

THE CEILING

FINISHED FLOOR LEVEL	+13.20
SOFFIT, GENERALLY	+16.20
CLEAR HEIGHT	3.00 m
STRUCTURAL ZONE OVER	300 mm
FLOOR TO FLOOR	3.30 m
BULKHEADS SHOWN	1 wet rooms
BULKHEAD DEPTH	by the services engineer
LIGHT FITTINGS	see EL-200 series

GENERAL NOTES

1. The ceiling of the penthouse floor, seen from below. Drawn by running the floor plan with its sanitaryware, furniture, door swings and dimension chains switched off, so it cannot stop agreeing with A-104 when a partition moves.

2. Soffit is +16.20 throughout, 3.00 m clear, under a 300 mm structural zone. Any local drop below that is a bulkhead and is shown as one.

3. A bulkhead is drawn over every room the plan calls wet, because that is where the drainage runs. The outline is the room; the depth, the exact extent and everything inside it are the services engineer's and are set on the ME and PL series.

4. No light fitting is drawn. Fittings, switching and emergency provision are the EL-200 series; a layout invented here would only have to be thrown away.

5. Ceiling finishes, board type, moisture resistance in the wet rooms and access panels are specification, not geometry, and are not set on this sheet.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

REFLECTED CEILING PLAN — PENTHOUSE FLOOR

DRAWING No	REVISION	SCALE	DATE
ARC-404	**P19**	**1:50 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor

EXTERNAL WORKS & LANDSCAPE

LEVEL -0.50 garden, +0.00 villa · 1:75 @ A1 · METRES

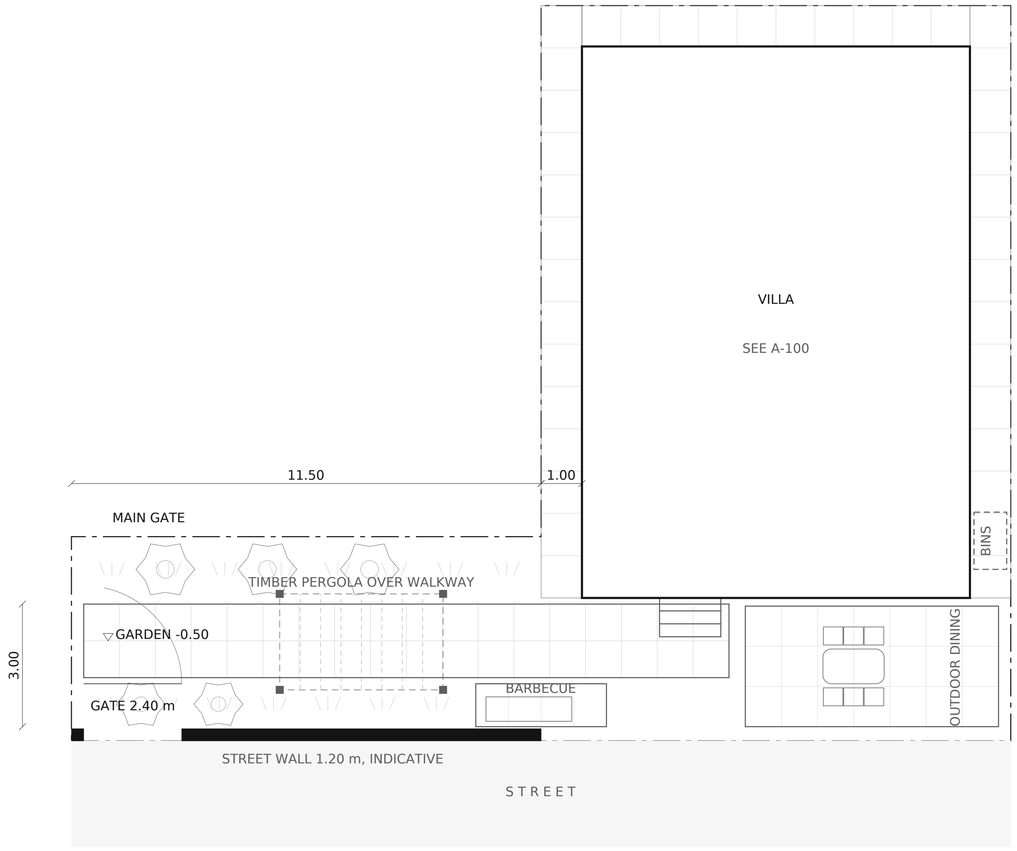

GRAPHIC SCALE 1:75

0 2 4 6 8 10 m

N

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

AREA SCHEDULE

PAVED WALK	28.4 m²
FORECOURT	18.3 m²
BARBECUE TERRACE	3.4 m²
SIDE PASSAGES	38.5 m²
TURF	24.7 m²
TOTAL	**113.3 m²**
PERGOLA OVER THE WALK	9.4 m² timber
TREES	5 nr
STREET WALL	9.10 m at 1.20 m, indicative
GATE	2.40 m leaf
STEPS TO THE FRONT DOOR	3 risers
PLOT LESS THE VILLA	136.2 m²
NOT MEASURED HERE	23.0 m²

GENERAL NOTES

1. The garden as a trade package rather than as context. Every area is read from the constants A-000 draws from, so this sheet and the site plan cannot disagree about a width.

2. The three 1.00 m setbacks are our own land and are paved as side passages, reached from the forecourt on the east and the garden on the west. They are the largest paved item on the sheet.

3. The street wall is 1.20 m high and INDICATIVE: its height, its coping and its finish await the client, and its line awaits the measured survey. Nothing else on the sheet depends on it.

4. Paving materials, bedding, falls, sub-base, turf specification and irrigation are not set by the geometry and are not invented here. The quantities are ours; the specification is not.

5. The forecourt is overhung by the balcony for up to 1.95 m, which is what covers the front door without a porch. See A-000 and A-400.

6. The schedule measures ground cover, so the pergola is listed beside it rather than in it - it stands over paving already counted. 23.0 m² of the plot outside the villa is not measured here: margins, the bin standing and the entrance steps. It is shown rather than absorbed.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

EXTERNAL WORKS & LANDSCAPE

DRAWING No	REVISION	SCALE	DATE
ARC-700	**P19**	**1:75 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys
P18 2026-10-07 scheme A adopted: serpentine balcony on every plan; site named
P19 2026-10-07 serpentine waist deepened 0.75 to 1.35 m; 15.7 m² of balcony a floor
