MASTER DELIVERABLES LIST

81 DELIVERABLES · 5 LEVELS, 6 SLABS · STATUS DERIVED AT BUILD TIME

CODE	CL	STATUS	DELIVERABLE	SCALE
PACKAGE 0 — INFORMATION REQUIRED FROM OTHERS (3)				
SUR-001	X	· not started	Measured topographic and boundary survey	1:200
GEO-001	X	! blocked	Soil investigation and foundation recommendation	-
CLI-001	X	· not started	Exterior scheme selection - A, B or C	-
PACKAGE A — PRESENTATION AND ESTIMATION (8)				
A-01	D	+ issued	Exterior views - axonometric, three schemes	1:250
A-02	D	· not started	Interior cutaway axonometric - ground floor, +0.00	1:100
A-03	D	· not started	Interior cutaway axonometric - first floor, +3.30	1:100
A-04	D	· not started	Interior cutaway axonometric - second floor, +6.60	1:100
A-05	D	· not started	Interior cutaway axonometric - third floor, +9.90	1:100
A-06	D	· not started	Interior cutaway axonometric - penthouse floor, +13.20	1:100
A-07	D	· not started	Architectural design brief	-
A-08	X	! blocked	Cost estimation report - elemental	-
PACKAGE B — ARCHITECTURE (21)				
ARC-000	D	+ issued	Master deliverables list and document register	-
ARC-001	D	· not started	Cover sheet, project data and drawing index	-
ARC-002	L	· not started	General notes, symbols and code compliance matrix	-
ARC-100	D	+ issued	Context and master site plan	1:75
ARC-101	D	+ issued	Ground floor plan, +0.00	1:50
ARC-102	D	+ issued	First floor plan, +3.30	1:50
ARC-103	D	+ issued	Second floor plan, +6.60	1:50
ARC-104	D	+ issued	Third floor plan, +9.90	1:50
ARC-105	D	+ issued	Penthouse floor plan, +13.20	1:50
ARC-106	D	· not started	Roof plan over the penthouse, +16.45	1:50
ARC-200	D	+ issued	Facade elevations - all four faces, three schemes	1:50 / 1:75
ARC-300	D	+ issued	Longitudinal section A-A	1:50
ARC-301	D	· not started	Transverse section B-B	1:50
ARC-400	D	· not started	Reflected ceiling plan - ground floor, +0.00	1:50
ARC-401	D	· not started	Reflected ceiling plan - first floor, +3.30	1:50
ARC-402	D	· not started	Reflected ceiling plan - second floor, +6.60	1:50
ARC-403	D	· not started	Reflected ceiling plan - third floor, +9.90	1:50
ARC-404	D	· not started	Reflected ceiling plan - penthouse floor, +13.20	1:50
ARC-500	D	· not started	Door and window schedule	-
ARC-600	L	! blocked	Construction details	1:5 / 1:10
ARC-700	D	· not started	External works and landscape	1:75
PACKAGE C — STRUCTURE (12)				
STR-001	L	· not started	Structural notes, materials and design criteria	-
STR-100	L	! blocked	Excavation, grading and shoring	1:100
STR-101	L	! blocked	Foundation layout	1:50
STR-200	L	· not started	Column schedule and grid	1:50
STR-301	L	! blocked	Slab framing layout at +0.00	1:50
STR-302	L	! blocked	Slab framing layout at +3.30	1:50
STR-303	L	! blocked	Slab framing layout at +6.60	1:50
STR-304	L	! blocked	Slab framing layout at +9.90	1:50
STR-305	L	! blocked	Slab framing layout at +13.20	1:50
STR-306	L	! blocked	Slab framing layout at +16.45	1:50
STR-400	L	! blocked	Retaining and boundary walls	1:50
STR-500	L	! blocked	Cantilever balcony structure	1:20
PACKAGE D — BUILDING SERVICES (33)				
EL-100	L	· not started	Power and small power layout - ground floor, +0.00	1:50
EL-101	L	· not started	Power and small power layout - first floor, +3.30	1:50
EL-102	L	· not started	Power and small power layout - second floor, +6.60	1:50
EL-103	L	· not started	Power and small power layout - third floor, +9.90	1:50
EL-104	L	· not started	Power and small power layout - penthouse floor, +13.20	1:50
EL-200	L	· not started	Lighting and switching layout - ground floor, +0.00	1:50
EL-201	L	· not started	Lighting and switching layout - first floor, +3.30	1:50
EL-202	L	· not started	Lighting and switching layout - second floor, +6.60	1:50
EL-203	L	· not started	Lighting and switching layout - third floor, +9.90	1:50
EL-204	L	· not started	Lighting and switching layout - penthouse floor, +13.20	1:50
EL-300	L	· not started	Low voltage, data and security layout - ground floor, +0.00	1:50
EL-301	L	· not started	Low voltage, data and security layout - first floor, +3.30	1:50
EL-302	L	· not started	Low voltage, data and security layout - second floor, +6.60	1:50
EL-303	L	· not started	Low voltage, data and security layout - third floor, +9.90	1:50
EL-304	L	· not started	Low voltage, data and security layout - penthouse floor, +13.20	1:50
ME-100	L	· not started	HVAC layout - ground floor, +0.00	1:50
ME-101	L	· not started	HVAC layout - first floor, +3.30	1:50
ME-102	L	· not started	HVAC layout - second floor, +6.60	1:50
ME-103	L	· not started	HVAC layout - third floor, +9.90	1:50
ME-104	L	· not started	HVAC layout - penthouse floor, +13.20	1:50
PL-100	L	· not started	Water supply layout - ground floor, +0.00	1:50
PL-101	L	· not started	Water supply layout - first floor, +3.30	1:50
PL-102	L	· not started	Water supply layout - second floor, +6.60	1:50
PL-103	L	· not started	Water supply layout - third floor, +9.90	1:50
PL-104	L	· not started	Water supply layout - penthouse floor, +13.20	1:50
PL-200	L	· not started	Drainage layout - ground floor, +0.00	1:50
PL-201	L	· not started	Drainage layout - first floor, +3.30	1:50
PL-202	L	· not started	Drainage layout - second floor, +6.60	1:50
PL-203	L	· not started	Drainage layout - third floor, +9.90	1:50
PL-204	L	· not started	Drainage layout - penthouse floor, +13.20	1:50
EL-400	L	! blocked	Electrical single line diagram	Schematic
ME-200	L	! blocked	HVAC schematic and plant arrangement	Schematic
PL-300	L	! blocked	Drainage and water riser diagram	Schematic
PACKAGE E — QUANTITIES AND COST CONTROL (4)				
QS-001	D	! blocked	Bill of quantities - itemised, unpriced, by trade	-
QS-002	D	! blocked	Bill of materials	-
QS-003	L	! blocked	Material requisitions and specifications	-
QS-004	X	! blocked	Owner's cost baseline	-

+ ISSUED > IN PROGRESS ! BLOCKED · NOT STARTED

MASTER DELIVERABLES LIST

DOCUMENT CONTROL · PACKAGES 0 AND A TO E · STATUS DERIVED

THE SET AT A GLANCE

DELIVERABLES	81
ISSUED	10
IN PROGRESS	0
BLOCKED	20
NOT STARTED	51
LEVELS	5
STRUCTURAL SLABS	6
D — DERIVED	28
L — LAYOUT FOR OTHERS	48
X — EXTERNAL	5

GENERAL NOTES

1. Nothing is issued as engineering that has not been engineered. Class D is generated from geometry.py and is ours to issue. Class L is layout and coordination only, sized and certified by others. Class X cannot be produced here at all.

2. So the structural package carries foundation layouts on the real grid and column coordinates, and no reinforcement; the services package carries coordination layouts, and no load calculations.

3. Status is derived at build time from the issued set, never typed. A row naming a sheet nobody draws, or a document nobody writes, fails the checks rather than printing here.

4. Five levels, 6 structural slabs: the slab at +13.20 is the penthouse floor and the roof over the third floor at once.

5. Deliverable codes are the client's. Where one resolves to sheets already issued, the existing number is the cross reference — the bound set at P16 is not renumbered.

6. Blocked rows wait on the measured survey, the soil investigation, or the choice between exterior schemes A, B and C. None of the three can be settled from the drawings.

7. For the owner's own record, costing and construction information. Not a tender issue, and not for construction.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


MASTER DELIVERABLES LIST

DRAWING No	REVISION	SCALE	DATE
ARC-000	**P17**	**NTS**	**2026-10-07**

Document control — every status on this sheet is derived at build time from the issued set.
Do not scale; work to figured dimensions only.

REVISIONS

P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
P15 2026-10-07 exterior: two schemes, elevations and balcony curves
P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
P17 2026-10-07 ARC-000 deliverables list; title corrected to five storeys

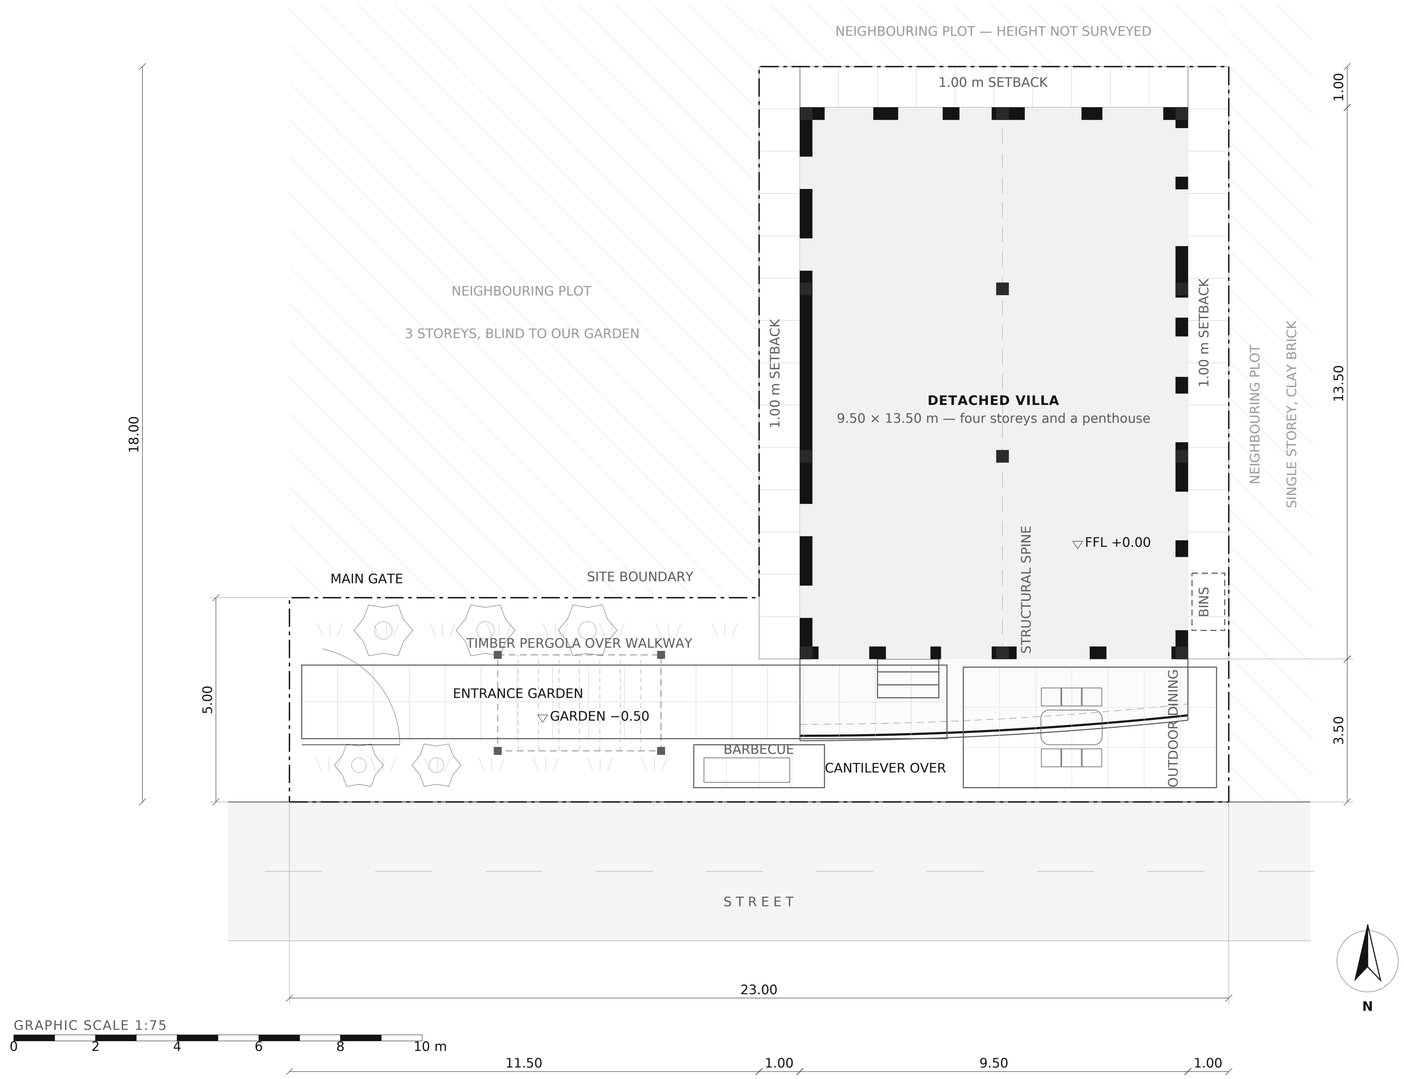

SITE PLAN — DETACHED VILLA

LEVEL +0.00 · 1:75 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

PLOT, SOUTH BAND 23.00 × 5.00	115.0 m²
PLOT, EAST PART 11.50 × 13.00	149.5 m²
TOTAL	**264.5 m²**
VILLA FOOTPRINT 9.50 × 13.50 M	128.2 m²
SITE COVERAGE	48.5 %
ENTRANCE GARDEN, WEST	57.5 m²
FORECOURT, IN FRONT	40.3 m²
SETBACKS, THREE SIDES	38.5 m²
GROSS INTERNAL AREA, FIVE STOREYS	505.2 m²

GENERAL NOTES

1. Final draft — layout agreed. The villa is detached: set back 1.00 m from the west, north and east boundaries, the three sides a neighbour stands on. The south is not set back — it faces the street across our own forecourt.

2. Footprint 9.50 × 13.50 m = 128.2 m² on a 264.5 m² plot, 48.5 % coverage against 63.0 % for the attached scheme at P4. Detaching costs 22 % of each floor and buys an open aspect on all four sides and no party wall.

3. The setbacks are our own land, so each is a 1.00 m paved side passage rather than a dead strip, reached from the forecourt on the east and from the entrance garden on the west.

4. The cantilever oversails the forecourt by 2.00 m at the west end and 1.50 m at the east, leaving at least 1.50 m clear to the street, and covers the front door and its three risers. Nothing projects over a boundary, but the overhang is subject to the local projection rule; confirm before construction.

5. The client's survey sketch recorded a 0.50 m step in the north boundary and a 5.50 m offset between the two blocks' north walls; the two cannot both be true. Resolved in favour of a straight boundary at 18.00. To be confirmed by measured survey before any work starts on site.

6. Structure is an RC frame on the grid shown, 300 mm columns on wall centrelines so none stands in a room. The A-300 enlargements are the last sheets still on the old 11.50 × 14.50 footprint.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SITE PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-000	**P16**	**1:75 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

- P13 2026-10-07 site plan redrawn for the detached villa
- P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
- P15 2026-10-07 exterior: two schemes, elevations and balcony curves
- P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey

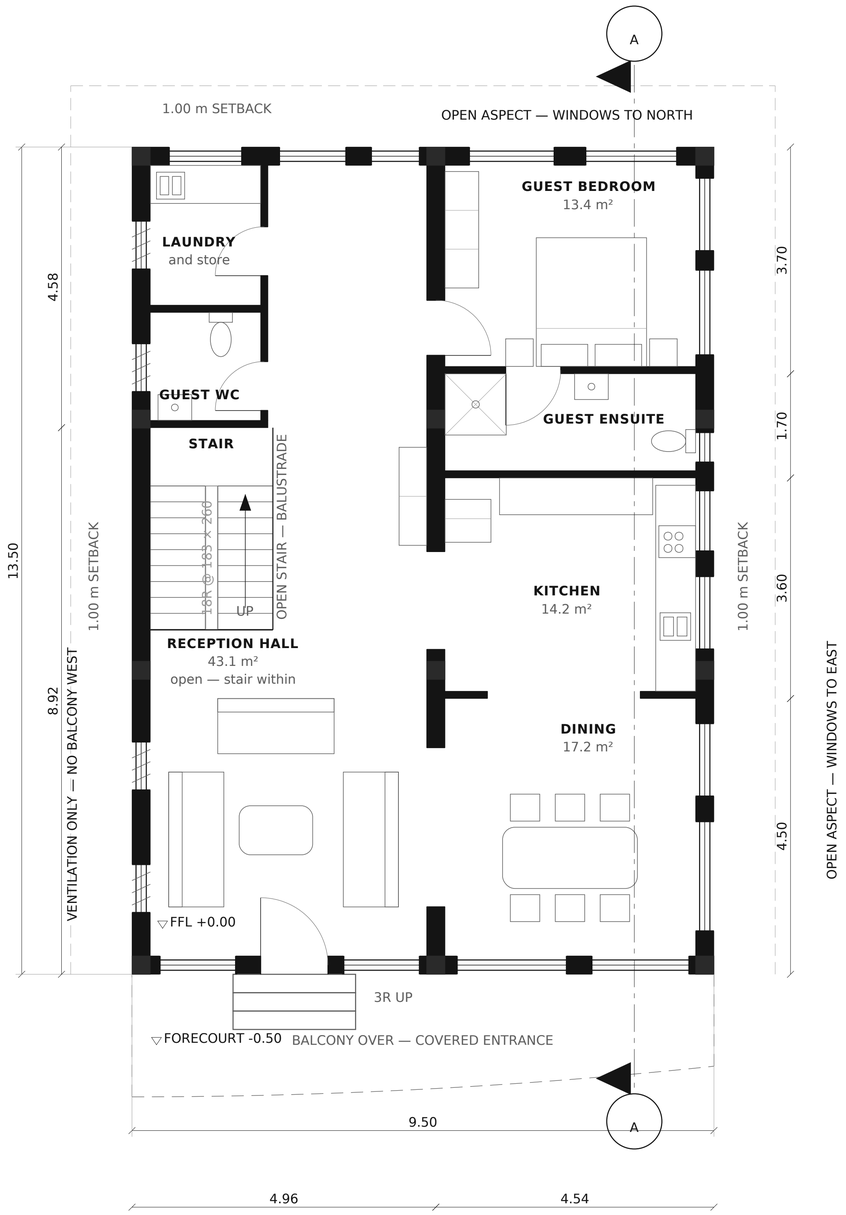



GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

GROUND FLOOR PLAN — DETACHED VILLA

LEVEL +0.00 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

RECEPTION HALL	43.1 m²
STAIR	6.6 m²
GUEST WC	3.2 m²
LAUNDRY	4.1 m²
DINING	17.2 m²
KITCHEN	14.2 m²
GUEST ENSUITE	6.5 m²
GUEST BEDROOM	13.4 m²
TOTAL	**108.3 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BEDROOMS	1 — the guest suite; 8 above
FLOOR ABOVE	+3.30

GENERAL NOTES

1. Final draft — layout agreed. The floor you receive people on: the family living is upstairs where the balconies are, so this one takes arrival, eating and a guest suite for anyone who cannot manage the stair.

2. Hall, dining and kitchen are one open sequence. The spine is cased open to both at 2.60 and 1.60 m, and the kitchen serves the dining through a 2.50 m opening rather than a door. Only the guest suite and the two service rooms are closed.

3. The reception hall is the whole west strip at 43.1 m², with the stair standing in it. It turns the corner behind the stair and runs on to the north wall, so the guest bedroom opens off the hall and there is no circulation room anywhere on the floor.

4. Guest WC, laundry and store are one block against the west wall, the only part of this floor that is walled off. East and north carry ordinary windows, the west louvred ventilation only.

5. The front door is in the hall's south wall, under the cantilever, which projects about 1.75 m there — so the entrance is covered without a porch being added to the elevation. Three risers up from the forecourt at −0.50.

6. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

7. The A-300 enlargements are the last sheets still on the old 11.50 × 14.50 footprint.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


GROUND FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-100	**P14**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P11 2026-10-07 penthouse: 2.51 m corridor outside the flat; living room to the face
P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan

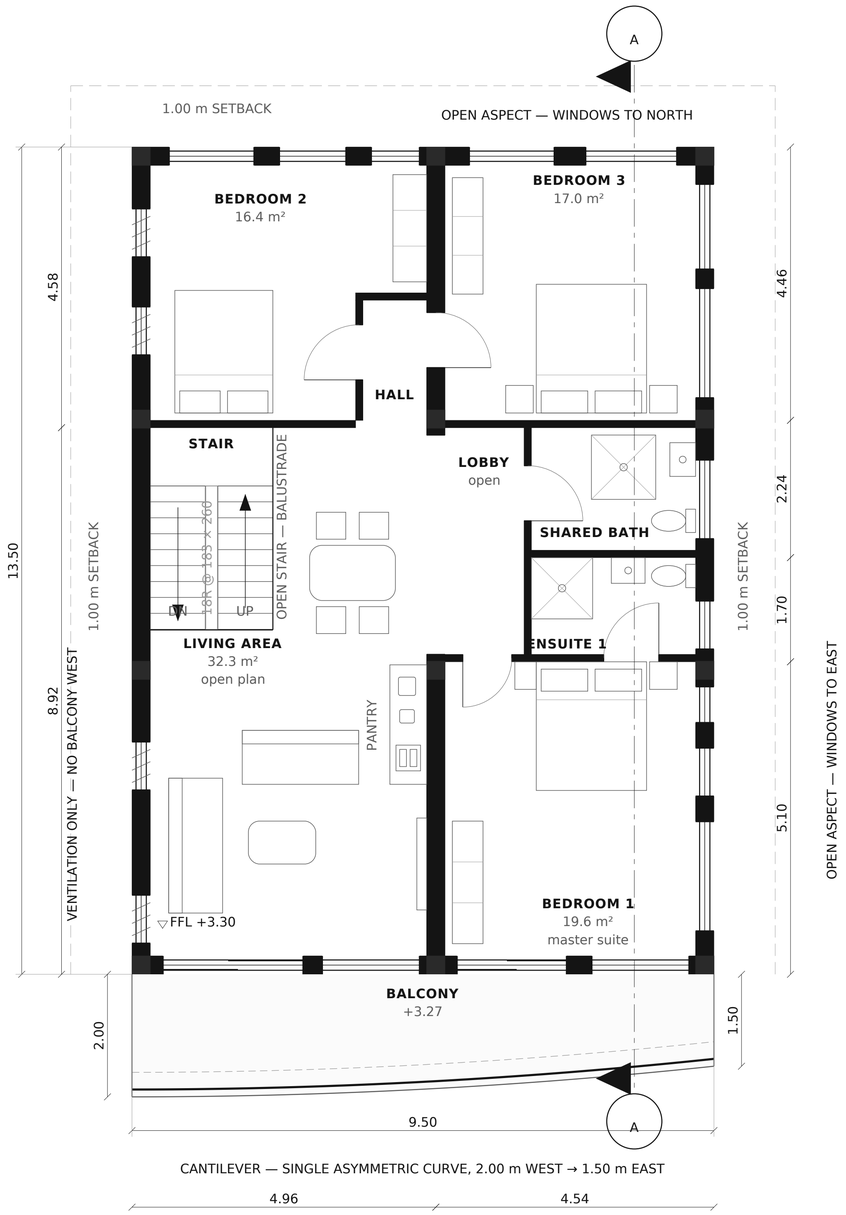



GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

FIRST FLOOR PLAN — DETACHED VILLA

LEVEL +3.30 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

AREA SCHEDULE

LIVING AREA	32.3 m²
STAIR	6.6 m²
BEDROOM 1 — MASTER	19.6 m²
BEDROOM 1 ENSUITE	4.2 m²
LOBBY	4.8 m²
SHARED BATH	5.4 m²
BEDROOM 2	16.4 m²
HALL	2.0 m²
BEDROOM 3	17.0 m²
TOTAL	**108.3 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BALCONY, EXTERNAL	17.4 m²
BEDROOMS	3 — the master, bedrooms 2 and 3
FLOOR ABOVE / BELOW	+6.60 / +0.00

GENERAL NOTES

1. Final draft — layout agreed. The living floor: a living area and bedrooms 1 to 3. The living area is 32.3 m² with the stair standing in it and the pantry open along the spine, opening through a sliding door onto the cantilever.

2. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

3. Bedroom 1 is the master at 19.6 m²: its north wall sits 1.30 m further north than the suite below it, and the shared bath gives up the same depth at 5.4 m².

4. The pantry is a counter against the solid stretch of spine, not the walled room the third floor has. The lobby has no wall either: the spine is opened 3.69 m between the columns, a downstand beam rather than a wall.

5. The west strip is otherwise the third floor's and the east strip the second's, so the wet rooms stack and the stair lines through. East and north carry ordinary windows, the west louvred ventilation only. The hall to the north bedrooms stops at its last door; the dead end beyond goes to bedroom 2, 16.4 m².

6. The cantilever runs on all three upper floors and the penthouse — the same curve, 2.00 m west sweeping to 1.50 m east, 17.4 m² — with sliding doors from the living area and bedroom 1.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


FIRST FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-101	**P14**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P11 2026-10-07 penthouse: 2.51 m corridor outside the flat; living room to the face
P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan

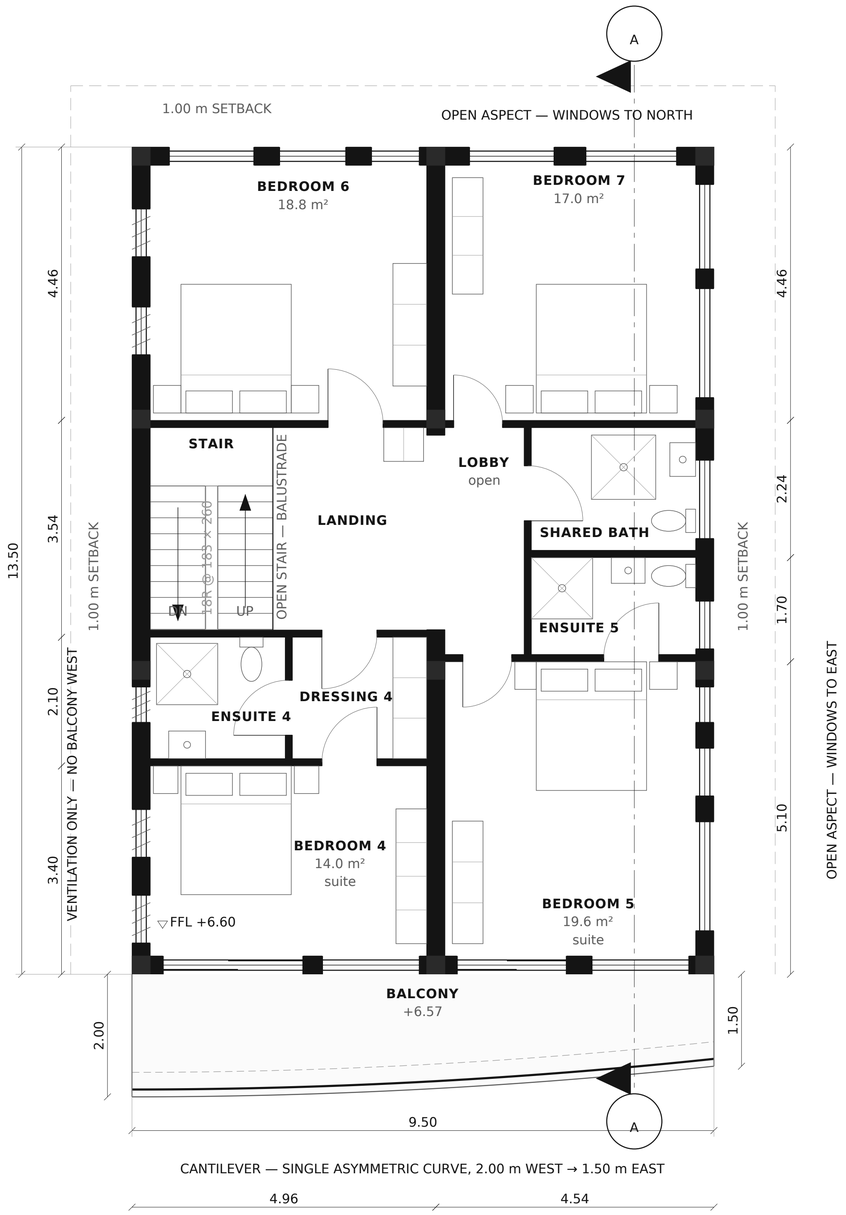





SECOND FLOOR PLAN — DETACHED VILLA

LEVEL +6.60 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

BEDROOM 4 — SUITE	14.0 m²
BEDROOM 4 ENSUITE	4.4 m²
BEDROOM 4 DRESSING	4.3 m²
BEDROOM 5 — SUITE	19.6 m²
BEDROOM 5 ENSUITE	4.2 m²
LOBBY	4.8 m²
STAIR	6.6 m²
LANDING	7.9 m²
SHARED BATH	5.4 m²
BEDROOM 6	18.8 m²
BEDROOM 7	17.0 m²
TOTAL	**107.0 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BALCONY, EXTERNAL	17.4 m²
BEDROOMS	4 — two of them suites
FLOOR ABOVE / BELOW	+9.90 / +3.30

GENERAL NOTES

1. Final draft — layout agreed. A bedroom floor: bedrooms 4 to 7, two of them suites, on the detached envelope.

2. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

3. Bedroom 4 takes the south-west with its ensuite and dressing behind; bedroom 5 the south-east, its ensuite off the bedroom.

4. The east strip is the first floor's, line for line — shared bath 5.4 m², lobby 4.8 m², bedroom 5 at 19.6 m² as its wall moves 1.30 m north. Every wet room and east window stacks, one drainage stack each, straight to the ground.

5. The lobby has no door: the spine is opened its whole length between the columns, so lobby and landing read as one space. It serves bedroom 5, the shared bath and bedroom 7. Bedroom 6 has the old hall — the whole north-west quarter, 18.8 m².

6. The cantilever is carried here too — the same curve, 2.00 m west to 1.50 m east, 17.4 m² — so it runs all three upper floors and the slabs stack. Both suites open onto it; a screen between the two is worth considering.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SECOND FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-102	**P14**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P11 2026-10-07 penthouse: 2.51 m corridor outside the flat; living room to the face
P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan

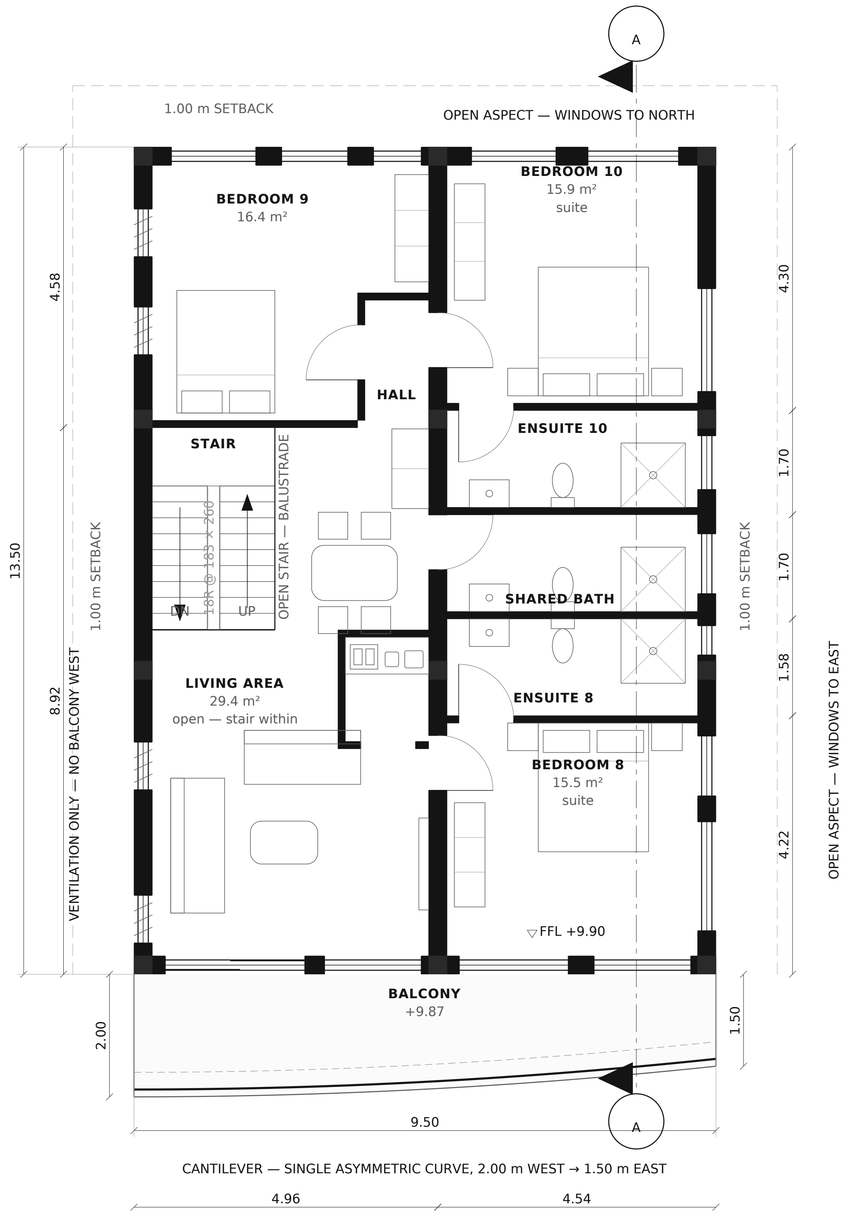





THIRD FLOOR PLAN — DETACHED VILLA

LEVEL +9.90 · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

AREA SCHEDULE

LIVING AREA	29.4 m²
STAIR	6.6 m²
HALL	2.0 m²
BEDROOM 8 — SUITE	15.5 m²
BEDROOM 8 ENSUITE	6.5 m²
SHARED BATH	6.5 m²
BEDROOM 10 ENSUITE	6.5 m²
BEDROOM 10 — SUITE	15.9 m²
BEDROOM 9	16.4 m²
TOTAL	**105.3 m²**
GROSS INTERNAL AREA, THIS FLOOR	114.8 m²
BALCONY, EXTERNAL	17.4 m²
ROOF OVER, TOP OF SLAB	+13.20

GENERAL NOTES

1. Final draft — layout agreed. The building is set back 1.00 m from the west, north and east boundaries; the south faces the street across our own forecourt. Detaching costs 22% of the floor — 114.8 m² against 147.3 — and removes the party wall, so one structural spine divides the plate.

2. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number.

3. The west strip south of bedroom 9 is one room: no wall divides the living area from the stair standing in it. The stair is a private villa stair — 900 mm flights, 18R at 183 × 260 — needing no enclosure, no smoke vent and no lift.

4. The south cantilever is reinforced concrete: one asymmetric curve bowed outward, 2.00 m at the west end sweeping away to 1.50 m at the east. Every point on the edge stands outside the line joining the two ends.

5. East and north carry ordinary windows. The east neighbour is a single storey in clay brick 1.00 m away, so they clear its roof by 1.20 m at the first floor. The west is louvred only — that neighbour is 3 storeys, and blind toward us.

6. Bedroom 8 and the shared bath open off the living area; bedrooms 9 and 10 off the hall, whose dead end goes to bedroom 9. Bedroom 10 has no balcony: it takes the north wall and two windows.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

THIRD FLOOR PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-103	**P16**	**1:50 @ A1**	**2026-10-07**


Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

- P13 2026-10-07 site plan redrawn for the detached villa
- P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
- P15 2026-10-07 exterior: two schemes, elevations and balcony curves
- P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey

PENTHOUSE PLAN — DETACHED VILLA

LEVEL +13.20 · 1:50 @ A1 · METRES

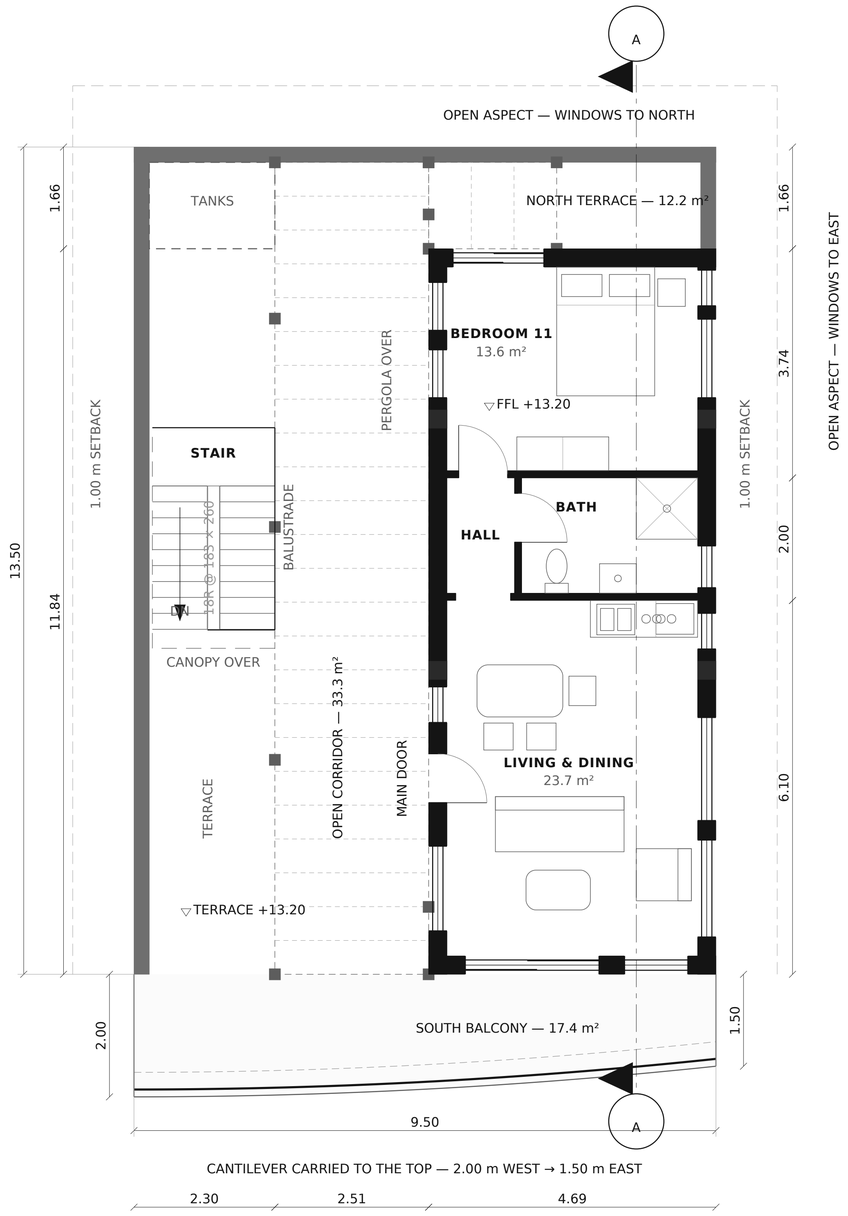

GRAPHIC SCALE 1:50

0 2 4 6 8 10 m

N

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

AREA SCHEDULE

LIVING AND DINING	23.7 m²
HALL	2.1 m²
BATH	5.4 m²
BEDROOM 11	13.6 m²
TOTAL	**44.8 m²**
GROSS INTERNAL AREA, FLAT	46.0 m²
SOUTH BALCONY, ON THE CANTILEVER	17.4 m²
SOUTH TERRACE, WEST OF THE CORRIDOR	11.5 m²
NORTH TERRACE	12.2 m²
OPEN CORRIDOR	33.3 m²
TOP OF PENTHOUSE SLAB	+16.45
FLOOR BELOW	+9.90

GENERAL NOTES

1. Bedrooms are numbered 1 to 11 through the house, south to north and west before east on each floor; the ground floor's room is the guest bedroom and carries no number. This is bedroom 11.

2. Final draft — layout agreed. The two open areas are joined outside the flat, down the west, by a corridor 2.51 m clear against the 2.00 m asked for, pergola over its whole length. The front door is off it.

3. 46.0 m² indoors; 17.4 m² of balcony on the cantilever, 11.5 m² of terrace by the stair, 12.2 m² north and 33.3 m² of corridor — all four run into one another.

4. The corridor passes east of the stair: the well is 2.00 m wide and hard against the west parapet, its half landing 1.65 m below this floor, so it stays open. Its east side is the flat's west wall, on the spine at x 17.46 — the one line on this side of the roof with a beam under it.

5. That leaves the flat 4.09 m clear, which will not take two bedrooms side by side: stacking them needs 12.06 m of the 13.50 m depth and leaves 1.44 m for both terraces. The second bedroom is what pays for the corridor.

6. The living room runs south to the building's face, so it opens straight onto the cantilever; y 3.65 is a grid line, so that wall sits on the columns and over the wall below. At +16.45 the penthouse is a fourth storey for most planning codes.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


PENTHOUSE PLAN — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-104	**P14**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P11 2026-10-07 penthouse: 2.51 m corridor outside the flat; living room to the face
P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan

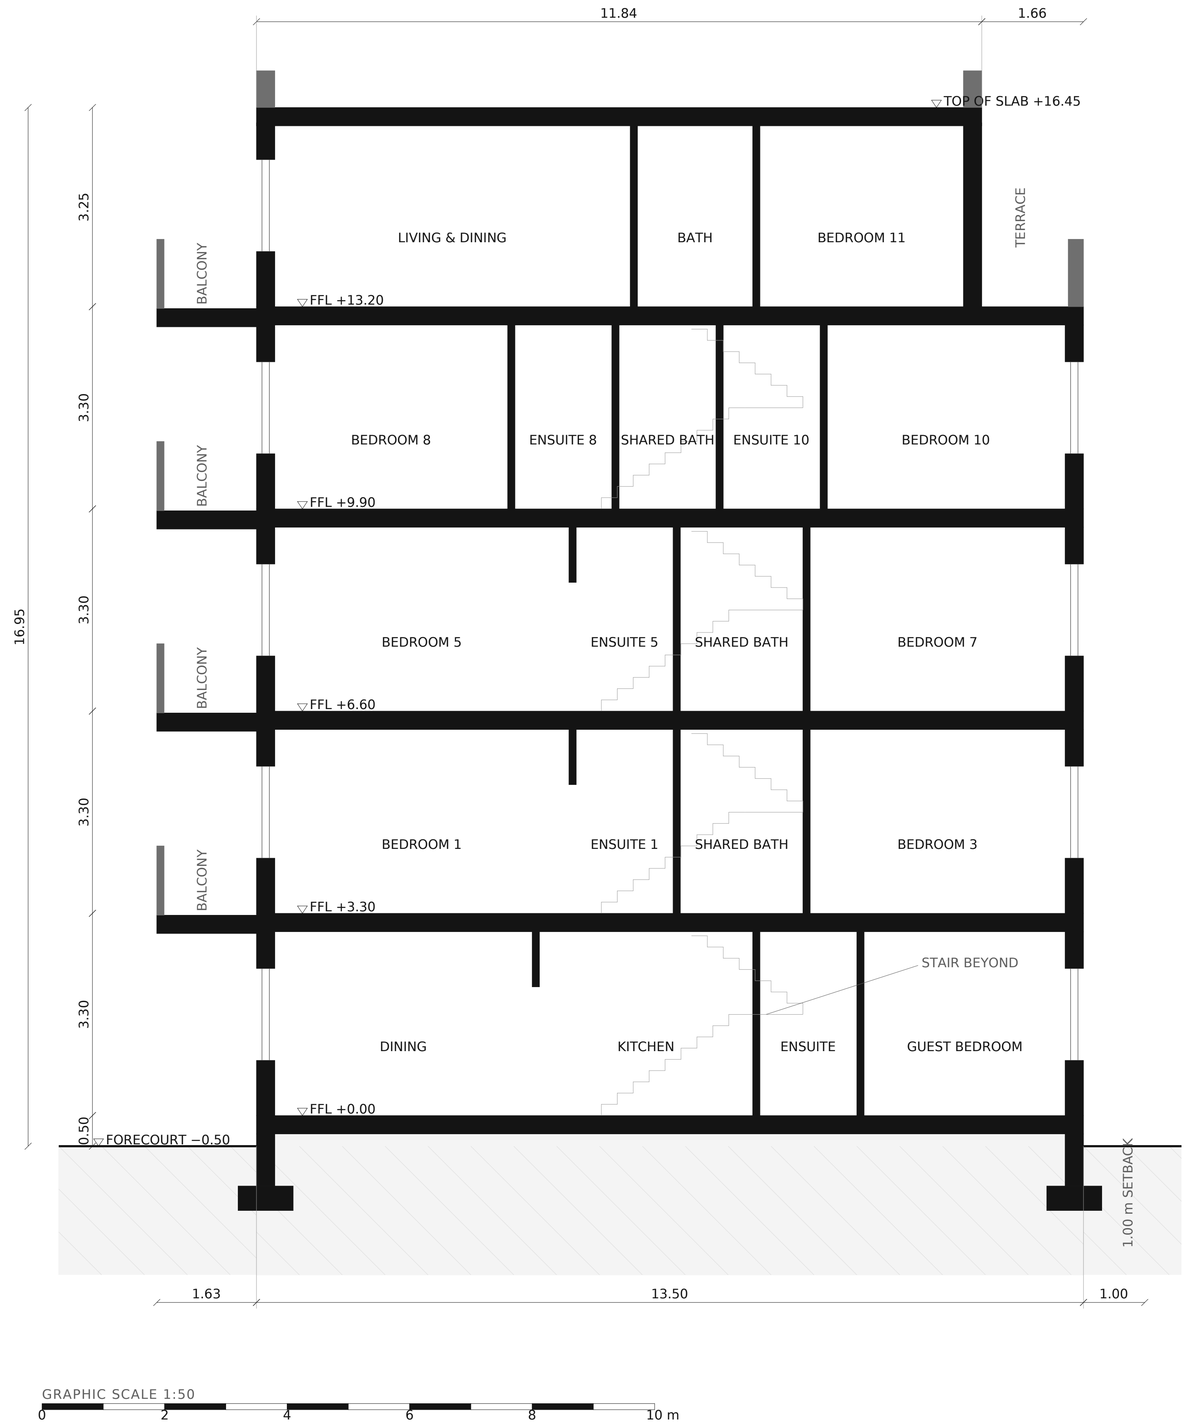

SECTION A–A — DETACHED VILLA

LEVEL looking west · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 — Finished floor level datum

LEVEL DATUMS

FORECOURT AND GARDEN	-0.50
GROUND FLOOR	+0.00
FIRST FLOOR	+3.30
SECOND FLOOR	+6.60
THIRD FLOOR	+9.90
PENTHOUSE FLOOR	+13.20
PENTHOUSE, TOP OF SLAB	+16.45
CLEAR CEILING HEIGHT	3.00 m
STRUCTURAL ZONE	0.30 m
OVERALL, GARDEN TO TOP	16.95 m

GENERAL NOTES

1. Final draft — layout agreed. Looking west, cut on the line marked A–A on every plan, at x 20.70. That line is not arbitrary: it is the one north-south cut that passes through a room at every level and through every wet room in the east strip, and it clears all three column lines, so the slabs are seen spanning rather than a column standing in the cut.

2. The wet rooms on the first and second floors sit one over the other, wall for wall — 8.60, 10.30 and 12.42 on both — so each drops a single drainage stack straight to the ground. The third floor divides the strip on its own lines and is shown as it is.

3. Flat slab on the column grid, 300 mm structural zone, giving 3.00 m clear at every level and 3.30 m floor to floor; the penthouse is 3.25 m floor to top of slab.

4. The south cantilever is carried on all three upper floors and the penthouse. It projects 1.63 m at this cut, against 2.00 m at the west end of the curve and 1.50 m at the east, with a glass balustrade at the slab edge.

5. The penthouse stands clear of the north edge, leaving the roof terrace beyond its north wall. The corridor that joins the two terraces runs west of this cut and does not appear; see A-104.

6. The stair is drawn in thin line beyond the cut, where it is seen through the open spine. Foundations are indicative only and subject to a ground investigation and the engineer's design.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

SECTION A–A — DETACHED VILLA

DRAWING No	REVISION	SCALE	DATE
A-200	**P14**	**1:50 @ A1**	**2026-10-07**

Final draft — layout agreed with the client; not for construction.
Do not scale; work to figured dimensions only.


REVISIONS

P11 2026-10-07 penthouse: 2.51 m corridor outside the flat; living room to the face
P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan



THE BALCONY CURVE IN PLAN — IT CANNOT SHOW IN ELEVATION

1.95 m DEEPEST · 0.75 m SHALLOWEST · 12.8 m² A FLOOR



GRAPHIC SCALE 1:100

0 2 4 m

SOUTH ELEVATION — SCHEME A “WAVE”

LEVEL street frontage · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

SCHEME A — WAVE

WALLS	warm limestone render
SLAB NOSING	rounded, 180 mm
COVE LIGHT	in the underside of the nosing
BALUSTRADE	clear glass, 120 mm inboard
FRAMES	bronze anodised
BALCONY CURVE	serpentine
PROJECTION	1.95 / 0.75 m
BALCONY AREA	12.8 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. Preliminary — the exterior only. The plans, site plan and section are agreed at P14 and nothing here changes them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the two schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. Scheme A takes its material from the contemporary reference: warm limestone render, a rounded slab nosing with a cove light tucked into its underside, clear glass balustrades and planting along the balcony edge. The four south bays read as glazed ribbons between the slabs.

4. The balcony curve is a serpentine — one full period across the frontage, 1.95 m deep at each end drawn in to 0.75 m at the waist. At the waist it is a planting ledge rather than somewhere to stand; the deep ends carry the furniture.

5. That shape costs area: 12.8 m² a floor against the 17.4 m² of the curve drawn today, so 18 m² over the four balcony levels. Adopting it re-issues A-000 and A-101 to A-104, which carry the balcony in plan.

6. The balconies do not wrap the corner as the reference does: the 1.00 m setbacks forbid anything projecting west, north or east, so the cantilever stays on the street frontage.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

SOUTH ELEVATION — SCHEME A “WAVE”

DRAWING No	REVISION	SCALE	DATE
A-400	**P15**	**1:50 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

- P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
- P13 2026-10-07 site plan redrawn for the detached villa
- P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
- P15 2026-10-07 exterior: two schemes, elevations and balcony curves



SIDE & REAR ELEVATIONS — SCHEME A “WAVE”

LEVEL east, north and west · 1:75 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

SCHEME A — WAVE

WALLS	warm limestone render
SLAB NOSING	rounded, 180 mm
COVE LIGHT	in the underside of the nosing
BALUSTRADE	clear glass, 120 mm inboard
FRAMES	bronze anodised
BALCONY CURVE	serpentine
PROJECTION	1.95 / 0.75 m
BALCONY AREA	12.8 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. Preliminary — the exterior only. The plans, site plan and section are agreed at P14 and nothing here changes them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the two schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. The east and north boundaries are open and carry ordinary windows on every floor. The west is the blind elevation: louvred ventilation only, drawn at high level, and nothing projects.

4. The penthouse stands back 4.81 m from the west and 1.66 m from the north, so on those two faces it is drawn in thin line behind the roof terrace parapet.

5. The balcony appears on the street frontage only and so does not show on any of these three faces.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SIDE & REAR ELEVATIONS — SCHEME A “WAVE”

DRAWING No	REVISION	SCALE	DATE
A-401	**P15**	**1:75 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.


REVISIONS

P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
P15 2026-10-07 exterior: two schemes, elevations and balcony curves

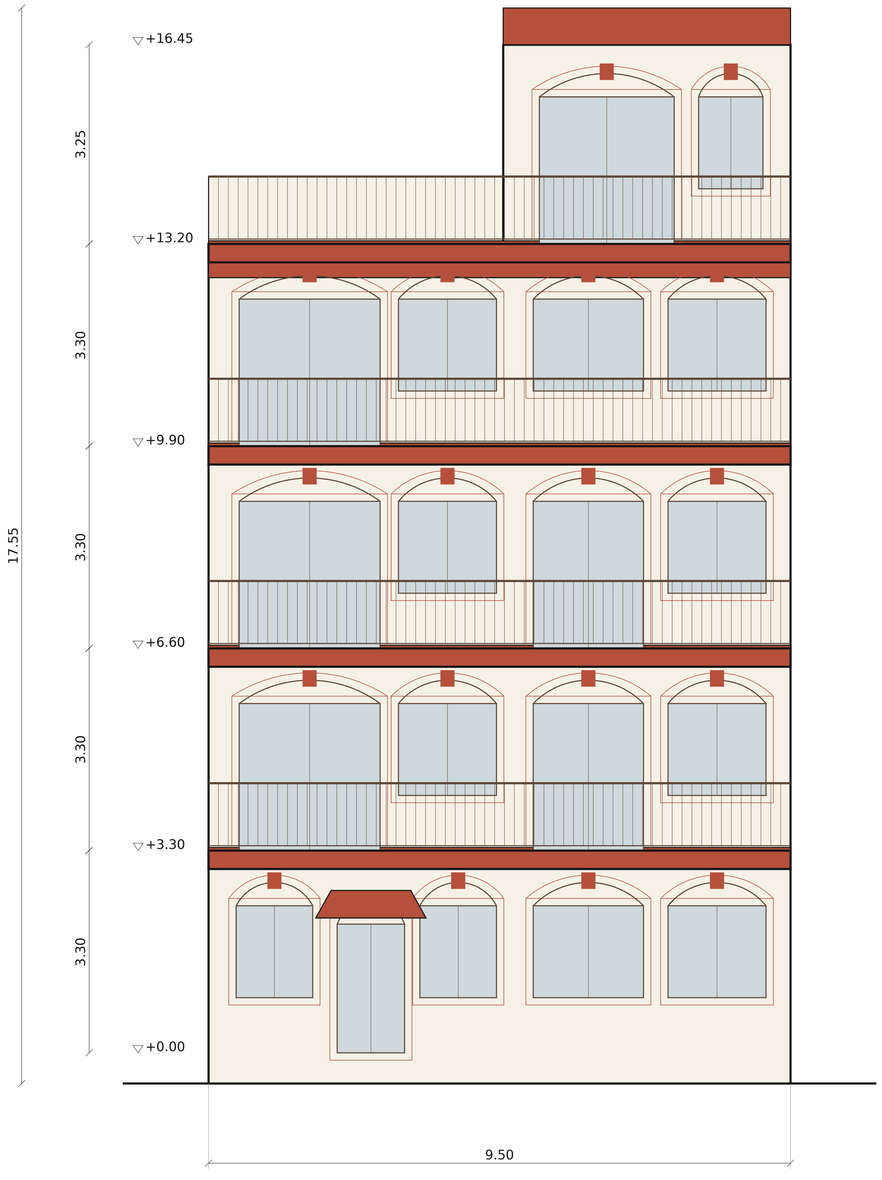

THE BALCONY CURVE IN PLAN — IT CANNOT SHOW IN ELEVATION

1.95 m DEEPEST · 0.90 m SHALLOWEST · 11.2 m² A FLOOR



GRAPHIC SCALE 1:100

0 2 4 m

SOUTH ELEVATION — SCHEME B “ARCADE”

LEVEL street frontage · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

SCHEME B — ARCADE

WALLS	ivory render, terracotta trim
FLOOR BANDS	350 mm at every level
OPENINGS	round arched, keystone
BALUSTRADE	wrought iron
FRAMES	dark stained timber
BALCONY CURVE	bowed centre bay
PROJECTION	1.95 / 0.90 m
BALCONY AREA	11.2 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. Preliminary — the exterior only. The plans, site plan and section are agreed at P14 and nothing here changes them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the two schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. Scheme B takes its ornament, not its shape, from the classical reference: ivory render with terracotta bands at every floor line, moulded surrounds, round-arched heads with keystones, and wrought-iron balustrade panels on the same cantilever.

4. The entrance is a recessed arched porch with a tiled hood, not a projecting portico. The cantilever already gives 1.96 m of cover over the front door and the forecourt has no room for one.

5. The balcony curve is a bowed centre bay — flanks at 0.90 m with a 5.00 m bow swelling to 1.95 m, blended so the bow meets the flanks tangentially. Centred on the frontage rather than the door, because symmetry is the whole character of the scheme.

6. It costs more area than scheme A: 11.2 m² a floor, 25 m² over the four levels. Adopting it re-issues A-000 and A-101 to A-104.

7. No pitched roof and no dome. Both raise the building, and at +16.45 the penthouse is already a fourth storey for most planning codes.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

SOUTH ELEVATION — SCHEME B “ARCADE”

DRAWING No	REVISION	SCALE	DATE
A-410	**P15**	**1:50 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
P15 2026-10-07 exterior: two schemes, elevations and balcony curves

SIDE & REAR ELEVATIONS — SCHEME B “ARCADE”

LEVEL east, north and west · 1:75 @ A1 · METRES

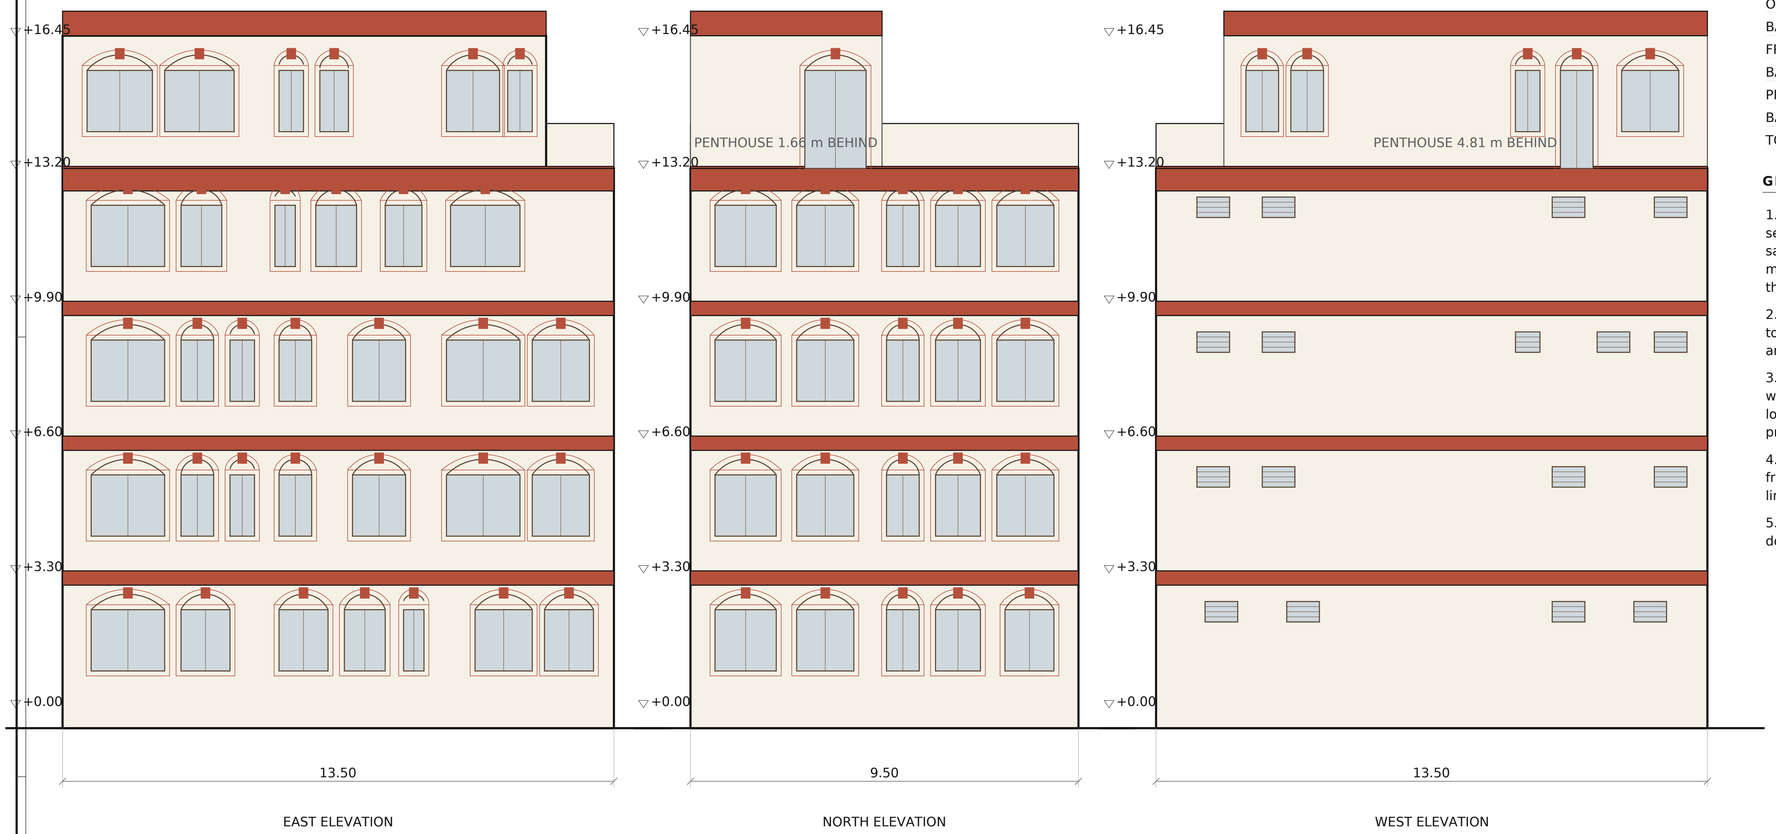

EAST ELEVATION

NORTH ELEVATION

WEST ELEVATION

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

SCHEME B — ARCADE

WALLS	ivory render, terracotta trim
FLOOR BANDS	350 mm at every level
OPENINGS	round arched, keystone
BALUSTRADE	wrought iron
FRAMES	dark stained timber
BALCONY CURVE	bowed centre bay
PROJECTION	1.95 / 0.90 m
BALCONY AREA	11.2 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. Preliminary — the exterior only. The plans, site plan and section are agreed at P14 and nothing here changes them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the two schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. The east and north boundaries are open and carry ordinary windows on every floor. The west is the blind elevation: louvred ventilation only, drawn at high level, and nothing projects.

4. The penthouse stands back 4.81 m from the west and 1.66 m from the north, so on those two faces it is drawn in thin line behind the roof terrace parapet.

5. The balcony appears on the street frontage only and so does not show on any of these three faces.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

SIDE & REAR ELEVATIONS — SCHEME B “ARCADE”

DRAWING No	REVISION	SCALE	DATE
A-411	**P15**	**1:75 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

- P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
- P13 2026-10-07 site plan redrawn for the detached villa
- P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
- P15 2026-10-07 exterior: two schemes, elevations and balcony curves



THE BALCONY CURVE IN PLAN — IT CANNOT SHOW IN ELEVATION

1.95 m DEEPEST · 0.90 m SHALLOWEST · 14.9 m² A FLOOR



GRAPHIC SCALE 1:100

0 2 4 m

SOUTH ELEVATION — SCHEME C “FACET”

LEVEL street frontage · 1:50 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- +0.00 Finished floor level datum

SCHEME C — FACET

WALLS	warm limestone render
SLAB NOSING	rounded, 180 mm
COVE LIGHT	in the underside of the nosing
BALUSTRADE	clear glass, 120 mm inboard
FRAMES	bronze anodised
BALCONY CURVE	straight runs, radiused
PROJECTION	1.95 / 0.90 m
STRAIGHT FORMWORK	7.10 of 9.50 m
BALCONY AREA	14.9 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. Preliminary — the exterior only. The plans, site plan and section are agreed at P14 and nothing here changes them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the two schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. Scheme C is scheme A's skin exactly — warm limestone, cove-lit slab nosings, glass balustrades, planting, the same arched ground floor. Only the balcony curve differs, which is the whole point of putting it beside A.

4. The curve is the serpentine built out of straight runs: 2.40 m flat at 1.95 m deep at each end, a flat waist at 0.90 m in the middle, and 1.20 m radiused transitions between. Every joint is a tangent, so from the street the eye still reads one continuous edge.

5. Two things recommend it over the true serpentine. The formwork is straight for 7.10 m of the 9.50 m span rather than curved end to end. And because the deep runs are flat rather than passing through their depth, it carries 14.9 m² a floor against the serpentine's 12.8 — 8 m² more over the four balcony levels.

6. It still costs area against the curve drawn today: 17.4 m² a floor becomes 14.9. Adopting it re-issues A-000 and A-101 to A-104, which carry the balcony in plan.

7. The balconies do not wrap the corner: the 1.00 m setbacks forbid anything projecting west, north or east, so the cantilever stays on the street frontage.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SOUTH ELEVATION — SCHEME C “FACET”

DRAWING No	REVISION	SCALE	DATE
A-420	**P15**	**1:50 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
P15 2026-10-07 exterior: two schemes, elevations and balcony curves

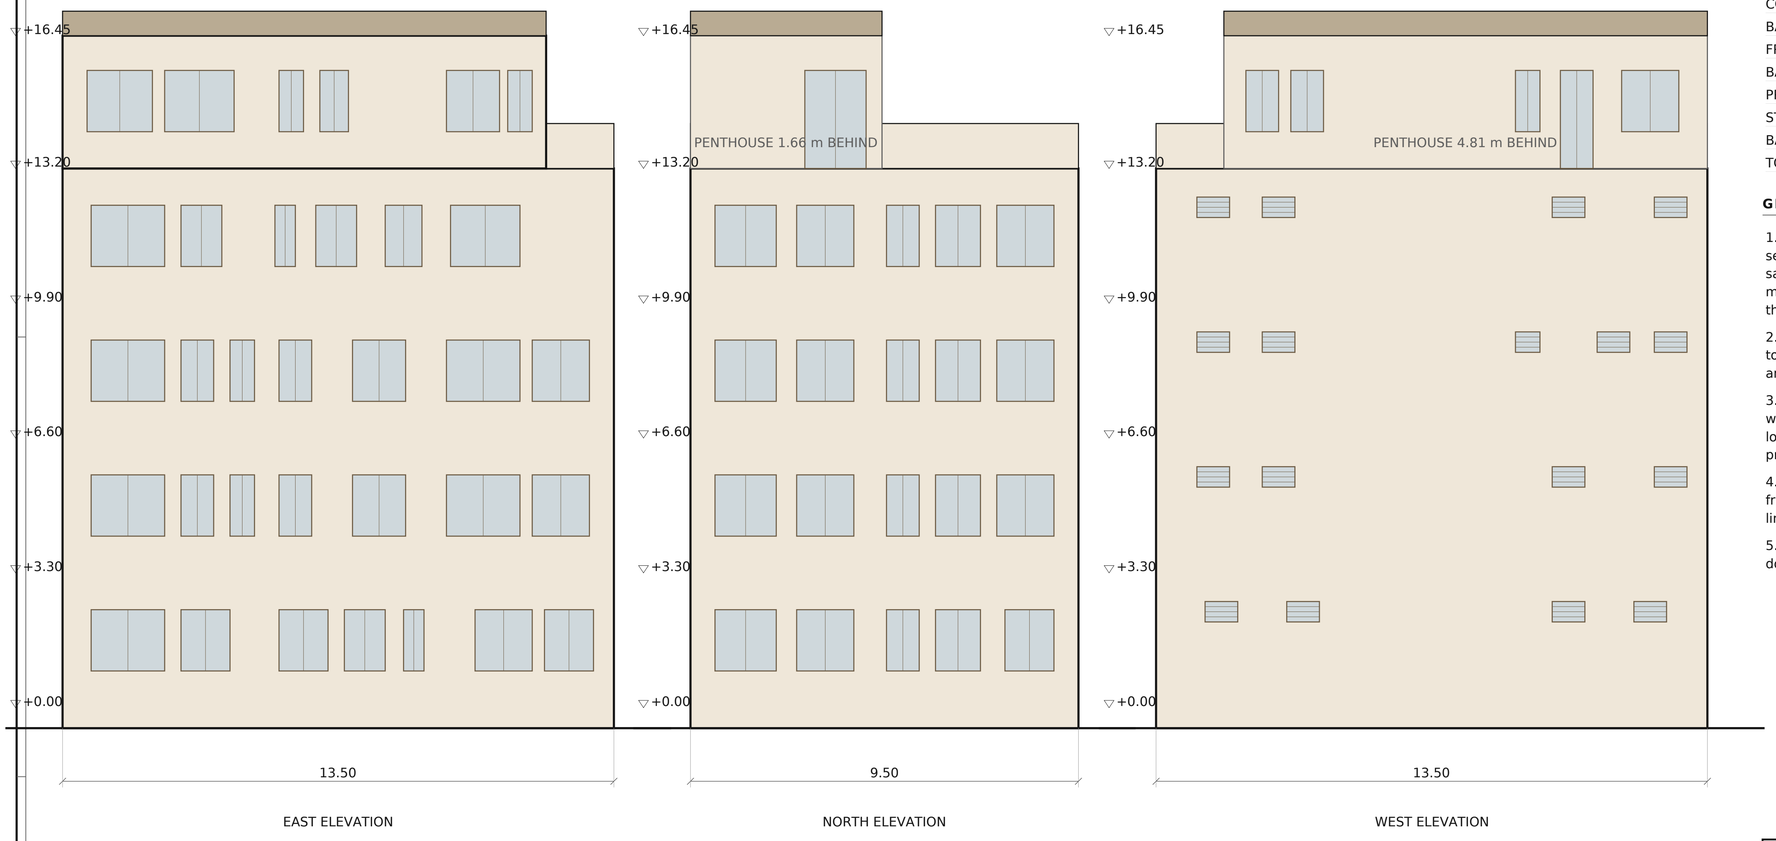

SIDE & REAR ELEVATIONS — SCHEME C “FACET”

LEVEL east, north and west · 1:75 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- +0.00 Finished floor level datum

SCHEME C — FACET

WALLS	warm limestone render
SLAB NOSING	rounded, 180 mm
COVE LIGHT	in the underside of the nosing
BALUSTRADE	clear glass, 120 mm inboard
FRAMES	bronze anodised
BALCONY CURVE	straight runs, radiused
PROJECTION	1.95 / 0.90 m
STRAIGHT FORMWORK	7.10 of 9.50 m
BALCONY AREA	14.9 m² a floor
TOP OF BUILDING	+17.05

GENERAL NOTES

1. Preliminary — the exterior only. The plans, site plan and section are agreed at P14 and nothing here changes them: same five levels, same 9.50 × 13.50 m footprint, same 1.00 m setbacks, same openings. Only the skin differs between the two schemes.

2. Every opening drawn here is read from the plan it belongs to rather than redrawn, and checks.py fails the build if an elevation ever shows one the plan does not have.

3. The east and north boundaries are open and carry ordinary windows on every floor. The west is the blind elevation: louvred ventilation only, drawn at high level, and nothing projects.

4. The penthouse stands back 4.81 m from the west and 1.66 m from the north, so on those two faces it is drawn in thin line behind the roof terrace parapet.

5. The balcony appears on the street frontage only and so does not show on any of these three faces.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


SIDE & REAR ELEVATIONS — SCHEME C “FACET”

DRAWING No	REVISION	SCALE	DATE
A-421	**P15**	**1:75 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P12 2026-10-07 bedrooms numbered 1-11; all five floors issued as final draft
P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
P15 2026-10-07 exterior: two schemes, elevations and balcony curves

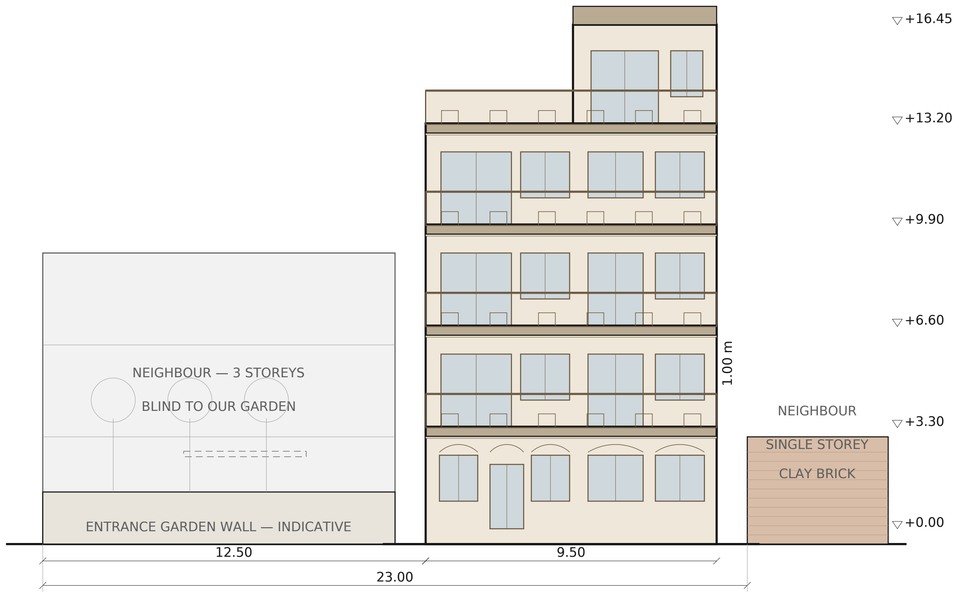

SCHEME A — WAVE

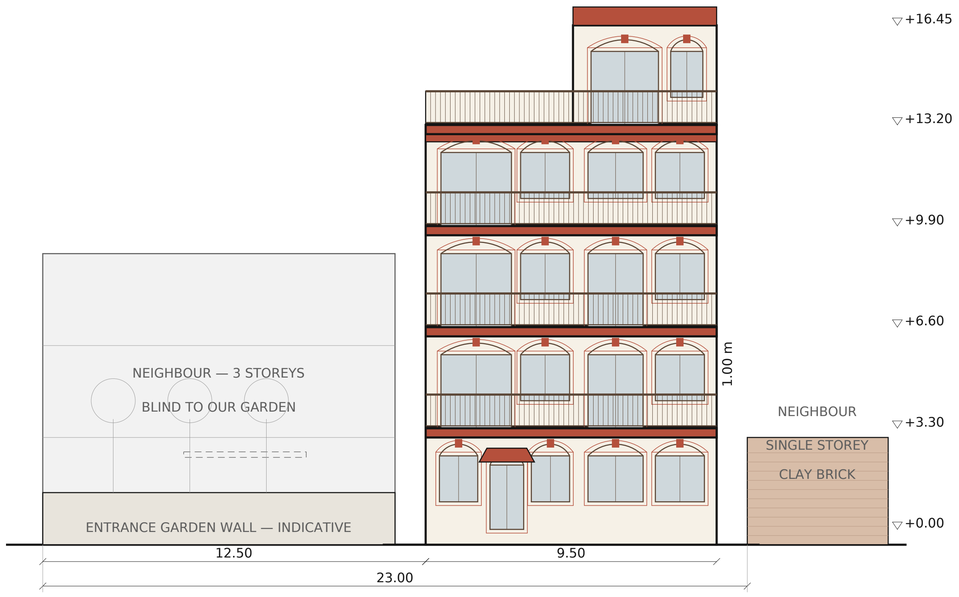

SCHEME B — ARCADE

GRAPHIC SCALE 1:100

0 2 4 6 8 10 m

STREET ELEVATION IN CONTEXT

LEVEL both schemes, as surveyed · 1:100 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

AS SURVEYED

PLOT WIDTH	23.00 m
ENTRANCE GARDEN, WEST	11.50 m
VILLA FRONTAGE	9.50 m
SIDE PASSAGE, EAST	1.00 m
WEST NEIGHBOUR	3 storeys, blind
EAST NEIGHBOUR	1 storey, clay brick
NORTH NEIGHBOUR	1 storey
OUR TOP OF BUILDING	+17.05
WE STAND OVER THE EAST	14.05 m

GENERAL NOTES

1. Preliminary — the exterior only, and the first drawing in the set to show the villa against the houses it actually stands between.

2. The house is not in the middle of its plot. It sits hard against the east boundary with a 1.00 m paved side passage, and the whole 11.50 m entrance garden is on the west, gated from the west boundary with a walk running east to the front door.

3. East: a single storey in clay brick, 1.00 m away. That is what lets the east wall be glazed at all — our lowest east sill at +4.20 clears its roof by 1.20 m. We stand 14.05 m over it, which is worth seeing before the elevations are agreed.

4. West: 3 storeys and blind toward us, drawn in thin line because it stands back behind the garden. Nothing of ours opens that way in any case — the west wall takes louvred ventilation only.

5. North: a single storey as well, confirmed by the client and not drawn on this south-facing view. The north wall carries windows on all five levels; only the ground floor looks at anything, and from +3.30 up they clear its roof as the east windows clear the east neighbour's.

6. The garden wall height is indicative and awaits the client's choice. Boundaries to be confirmed by measured survey.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING


STREET ELEVATION IN CONTEXT


DRAWING No	REVISION	SCALE	DATE
A-402	**P16**	**1:100 @ A1**	**2026-10-07**


Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
P15 2026-10-07 exterior: two schemes, elevations and balcony curves
P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey

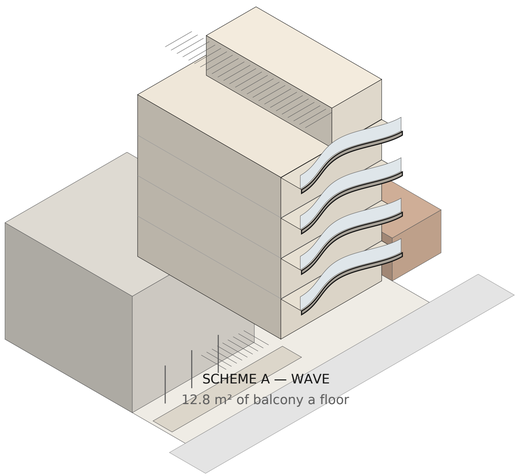

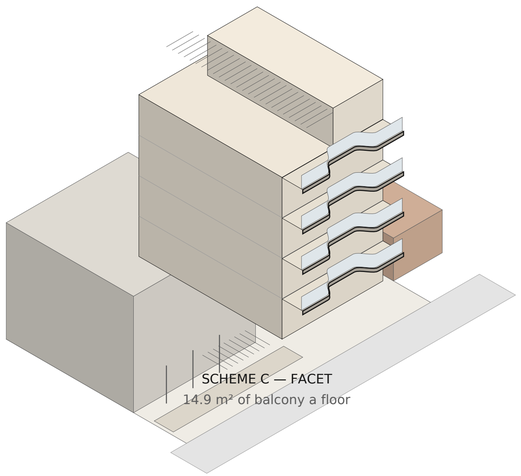

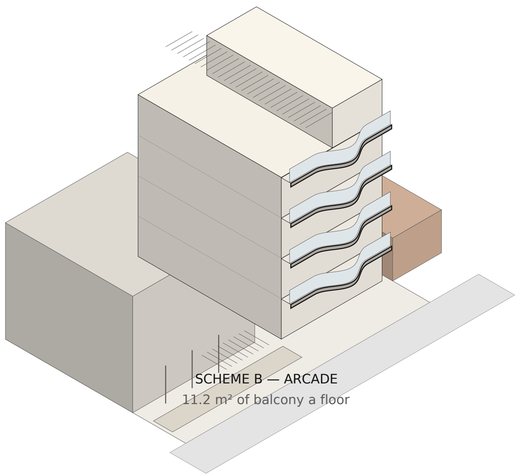

AXONOMETRIC — THREE BALCONY OPTIONS

LEVEL from the south-west · 1:250 @ A1 · METRES

KEY

- Masonry wall cut by section — 200 mm partition, 300 mm external / party
- Internal stud or block partition, 120 mm
- Terrace parapet, 250 mm × 1100 mm high
- Single leaf door, swing shown to opening side
- Glazed opening — arched head where noted
- Element above the cut plane (pergola, slab over)
- Void / open to sky
- ▽ +0.00 Finished floor level datum

THE FOUR CURVES

AGREED, DRAWN TODAY	17.4 m² a floor
A — SERPENTINE	12.8 m² a floor
C — FACET	14.9 m² a floor
B — BOWED CENTRE BAY	11.2 m² a floor
DEEPEST ALLOWED	2.00 m
SHALLOWEST USABLE	0.60 m
WEST NEIGHBOUR	3 storeys, blind
EAST NEIGHBOUR	1 storey, clay brick

GENERAL NOTES

1. Preliminary. Isometric from the south-west, which is the one corner that shows the street frontage, the blind west wall, the roof pergola and the entrance garden at once.

2. This is a projection, not a render: every line is a transform of the constants the plans are drawn from, so it cannot show a balcony, a garden or a neighbour that the drawings do not have.

3. All three sit on the real plot. The villa is hard against the east boundary with a 1.00 m side passage and the 11.50 m entrance garden on the west, the three-storey blind neighbour standing back behind it and the single-storey clay-brick one a metre to the east.

4. A and C wear the same skin, so the only difference between them is the curve — which is why they stand side by side here. B differs in ornament as well.

5. The balconies stop at the corner on all three: the 1.00 m setbacks forbid anything projecting west, north or east.

6. Faces are painted back to front rather than depth-sorted, so a detail may overlap where two surfaces nearly touch. The measured elevations A-400 to A-421 govern.

FIVE-STOREY VACATION VILLA — SHAMANDEEL, QUESNA, MENOUFIA, EGYPT

DRAWING

AXONOMETRIC — THREE BALCONY OPTIONS

DRAWING No	REVISION	SCALE	DATE
A-430	**P16**	**1:250 @ A1**	**2026-10-07**

Preliminary design issue — not for construction.
Do not scale; work to figured dimensions only.

REVISIONS

P13 2026-10-07 site plan redrawn for the detached villa
P14 2026-10-07 section A-A recut through the east strip, and marked on every plan
P15 2026-10-07 exterior: two schemes, elevations and balcony curves
P16 2026-10-07 neighbours as surveyed: west 3 storeys and blind, east single storey
